

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jul 14, '24							Jul 21, '24							Jul 28, '24						
								F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T
1		30233 Carrollton Basin No.4																										
2																												
3		Two Week Look Ahead	9 days	Tue 9/3/24	Fri 9/13/24																							
4																												
5		Sewer Rehabilitation																										
6																												
7		2800 Eagle	15 days	Wed 8/28/24	Tue 9/17/24																							
8		Sewer House Connections	5 days	Wed 9/4/24	Tue 9/10/24	12																						
9		Restoration	5 days	Wed 9/11/24	Tue 9/17/24	8																						
10																												
11		2700 Eagle	5 days	Wed 9/4/24	Tue 9/10/24																							
12		Sewer House Connections	1 day	Tue 9/3/24	Tue 9/3/24																							
13																												
14		1100 S Claiborne	4 days	Tue 9/3/24	Fri 9/6/24																							
15		Rework Sewer Point Repair	2 days	Tue 9/3/24	Wed 9/4/24																							
16		Post CCTV	1 day	Fri 9/6/24	Fri 9/6/24																							
17																												
18		CIPP																										
19																												
20		7200 S Claiborne	1 day	Thu 9/5/24	Thu 9/5/24																							
21		CCTV	1 day	Thu 9/5/24	Thu 9/5/24																							
22																												
23		1100 S Claiborne	1 day	Thu 9/12/24	Thu 9/12/24																							
24		CIPP	1 day	Thu 9/12/24	Thu 9/12/24																							
25																												
26		3800 Octavia	7 days	Tue 9/3/24	Wed 9/11/24																							
27		Post CCTV	1 day	Tue 9/3/24	Tue 9/3/24																							
28		CIPP	1 day	Wed 9/11/24	Wed 9/11/24																							
29																												
30		Roadway Restoration																										
31																												
32		300 Audubon	9 days	Tue 9/3/24	Fri 9/13/24																							
33		Restoration	9 days	Tue 9/3/24	Fri 9/13/24																							
34																												
35		400 Audubon	9 days	Tue 9/3/24	Fri 9/13/24																							
36		Restoration	9 days	Tue 9/3/24	Fri 9/13/24																							
37																												
38		1500 Norman C Francis	1 day	Tue 9/3/24	Tue 9/3/24																							


Project: 30233 Two Week Look
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jul 14, '24							Jul 21, '24							Jul 28, '24									
								F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F		
39		Asphalt	1 day	Tue 9/3/24	Tue 9/3/24																										
40																															
41		7400 Maple	1 day	Tue 9/3/24	Tue 9/3/24																										
42		Pour S/W	1 day	Tue 9/3/24	Tue 9/3/24																										




Project: 30233 Two Week Look Date: Fri 8/30/24	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

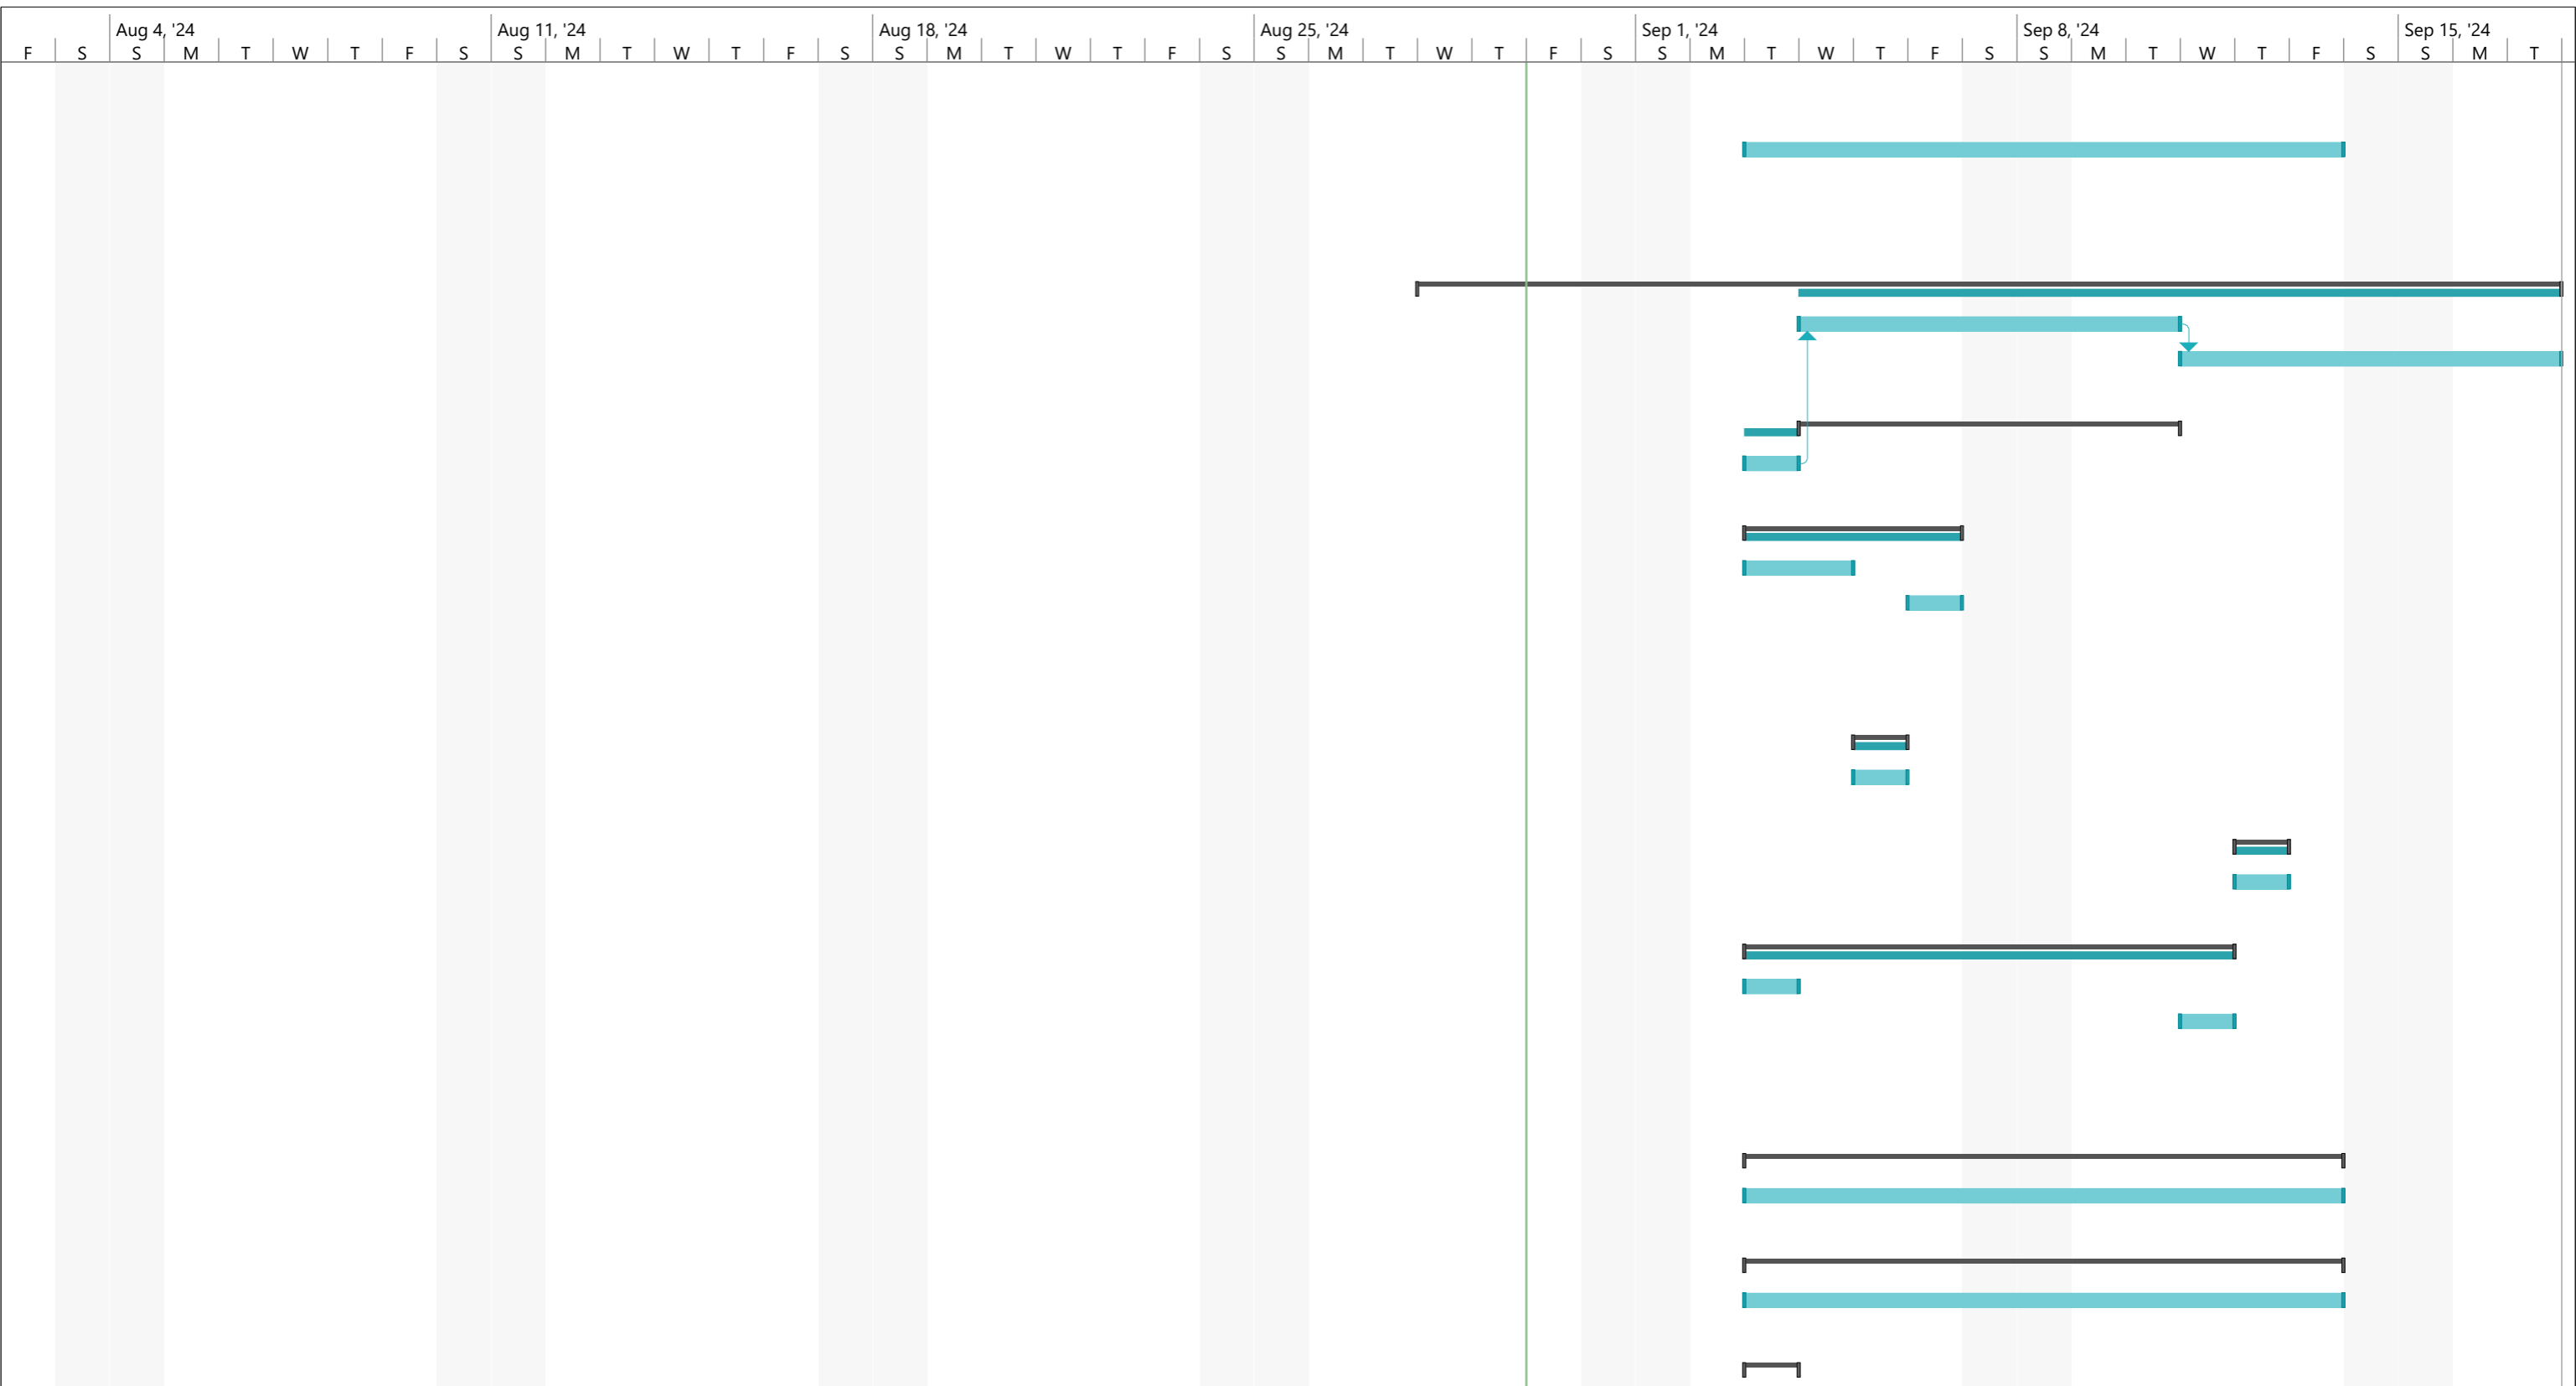

Project: 30233 Two Week Look
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			



Project: 30233 Two Week Look
 Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
