


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Aug 11, '24			Aug 18, '24			Aug 25, '24			Sep 1, '24			Sep 8, '24			
								T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
1	★	30261 Carrollton Basin No. 20	9 days	Tue 8/27/24	Fri 9/6/24																		
2	👤																						
3	★	Two Week Look Ahead	9 days	Tue 8/27/24	Fri 9/6/24																		
4	👤																						
5	★	CCTV	14 days	Tue 8/27/24	Fri 9/13/24																		
6	👤																						
7	★	8700 Olive St	12 days	Thu 8/29/24	Fri 9/13/24																		
8	★	Pre CCTV	1 day	Thu 8/29/24	Thu 8/29/24																		
9	★	Lateral Launch	1 day	Tue 9/10/24	Tue 9/10/24	15																	
10	👤	1400 Dante St	8 days	Fri 8/30/24	Tue 9/10/24																		
11	★	Pre CCTV	1 day	Fri 8/30/24	Fri 8/30/24	8																	
12	★	Lateral Launch	1 day	Tue 9/10/24	Tue 9/10/24	15																	
13	👤	1900 Dante St	6 days	Mon 9/2/24	Mon 9/9/24																		
14	★	Pre CCTV	1 day	Mon 9/2/24	Mon 9/2/24	11																	
15	★	Lateral Launch	1 day	Mon 9/9/24	Mon 9/9/24	21																	
16	👤	8300 Apple St	5 days	Tue 9/3/24	Mon 9/9/24																		
17	★	Pre CCTV	1 day	Tue 9/3/24	Tue 9/3/24	14																	
18	★	Lateral Launch	1 day	Mon 9/9/24	Mon 9/9/24	21																	
19	👤	9100 Olive St	3 days	Wed 9/4/24	Fri 9/6/24																		
20	★	Pre CCTV	1 day	Wed 9/4/24	Wed 9/4/24	17																	
21	★	Lateral Launch	1 day	Fri 9/6/24	Fri 9/6/24	23																	
22	👤	8500 Apple St	2 days	Thu 9/5/24	Fri 9/6/24																		
23	★	Pre CCTV	1 day	Thu 9/5/24	Thu 9/5/24	20																	
24	★	Lateral Launch	1 day	Fri 9/6/24	Fri 9/6/24	23																	

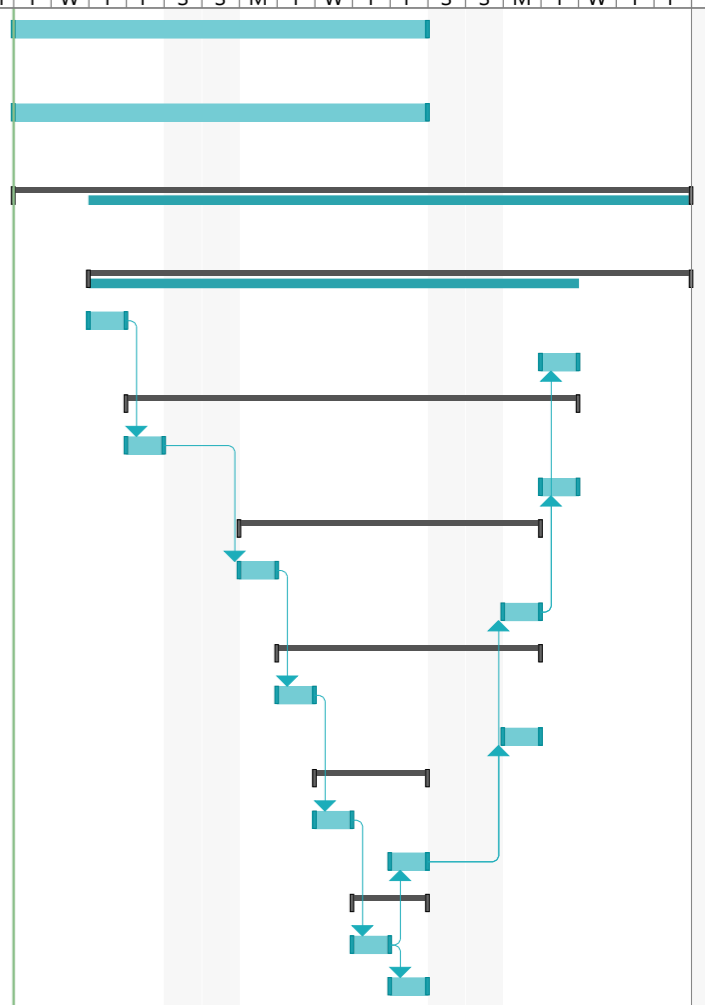

Project: 30261 Two Week Look
Date: Tue 8/27/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
