


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Jul 21, '24					Jul 28, '24					Aug 4, '24					Aug 11, '24					Aug 18, '24																		
								S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S				
1	?	30233 Carrollton Basin No. 4																																												
2	?																																													
3	?	Two Week Look Ahead	10 days	Mon 8/12/24	Fri 8/23/24																																									
4	?																																													
5	?	Sewer Rehabilitation																																												
6	?																																													
7	?	2800 Eagle St	10 days	Mon 8/12/24	Fri 8/23/24																																									
8	?	Sewer Main Installation	2 days	Mon 8/12/24	Tue 8/13/24																																									
9	?	Sewer House Connections	8 days	Wed 8/14/24	Fri 8/23/24	8																																								
10	?	Roadway Restoration																																												
11	?																																													
12	?	300 Audubon	5 days	Mon 8/12/24	Fri 8/16/24																																									
13	?	Roadway Restoration	5 days	Mon 8/12/24	Fri 8/16/24																																									
14	?																																													
15	?	400 Audubon	5 days	Mon 8/19/24	Fri 8/23/24																																									
16	?	Roadway Restoration	5 days	Mon 8/19/24	Fri 8/23/24																																									
17	?																																													
18	?	CCTV																																												
19	?																																													
20	?	7200 S Claiborne	1 day	Tue 8/13/24	Tue 8/13/24																																									
21	?	Post CCTV	1 day	Tue 8/13/24	Tue 8/13/24																																									
22	?																																													
23	?	1100 S Claiborne	1 day	Wed 8/14/24	Wed 8/14/24																																									
24	?	Post CCTV	1 day	Wed 8/14/24	Wed 8/14/24	21																																								
25	?																																													
26	?	CIPP	4 days	Mon 8/19/24	Thu 8/22/24																																									
27	?	1500 S Jeff Davis	1 day	Mon 8/19/24	Mon 8/19/24																																									
28	?	CIPP	1 day	Mon 8/19/24	Mon 8/19/24																																									
29	?	1700 S Jeff Davis	1 day	Tue 8/20/24	Tue 8/20/24																																									
30	?	CIPP	1 day	Tue 8/20/24	Tue 8/20/24	28																																								
31	?	2400 S Galvez	1 day	Wed 8/21/24	Wed 8/21/24		Pending Review																																							
32	?	CIPP	1 day	Wed 8/21/24	Wed 8/21/24	30																																								
33	?	2200 Lowerline	1 day	Thu 8/22/24	Thu 8/22/24		Pending Review																																							
34	?	CIPP	1 day	Thu 8/22/24	Thu 8/22/24	32																																								

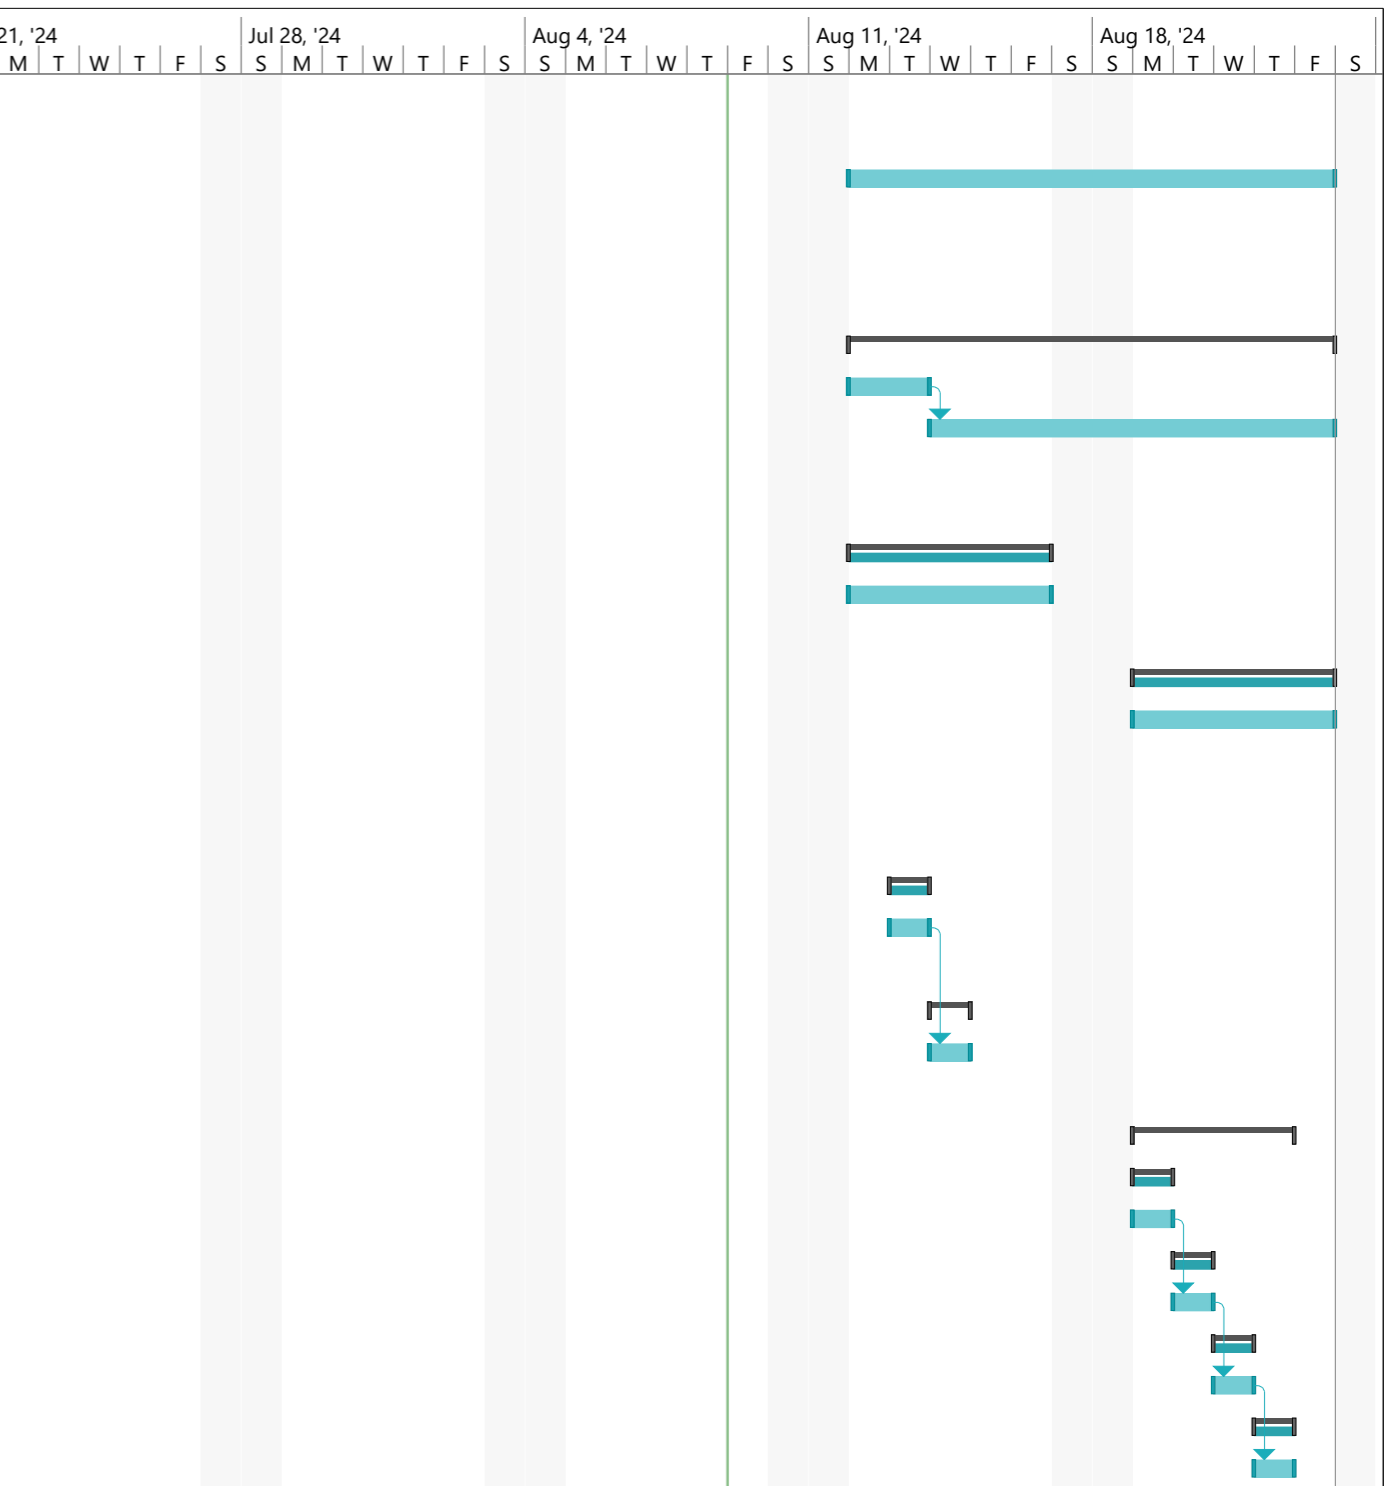

Project: 30256 Two Week Look
Date: Fri 8/9/24

Task: [Solid Blue Bar] Project Summary [Dashed Blue Bar] Inactive Task [Solid Black Bar] Inactive Milestone [Solid Black Bar] Inactive Summary [Grey Bar with Outline] Manual Task [Grey Bar with Outline] Manual Summary Rollup [Grey Bar with Outline] Manual Summary [Teal Bar with Outline] Start-only [Teal Bar with Gradient] Finish-only [Teal Bar with Gradient] External Tasks [Teal Bar with Gradient] External Milestone [Teal Bar with Gradient] External Milestone [Grey Diamond] Deadline [Green Arrow Down] Progress [Blue Line] Manual Progress [Teal Line]
