

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr '24				May '24				Jun '24				
								10	17	24	31	7	14	21	28	5	12	19	26	2
1		8100 Burthe	40 days	Mon 6/10/24	Fri 8/2/24															
2		Sewer	12 days	Mon 6/10/24	Tue 6/25/24		Doc													
3		Restoration	20 days	Mon 7/8/24	Fri 8/2/24		C&M													
4		8300 Freret	37 days	Wed 6/26/24	Thu 8/15/24															
5		Sewer	10 days	Wed 6/26/24	Tue 7/9/24	2	Doc													
6		Restoration	20 days	Fri 7/19/24	Thu 8/15/24		C&M													
7		8200 Freret	39 days	Thu 7/11/24	Tue 9/3/24															
8		Sewer	12 days	Wed 7/10/24	Thu 7/25/24	5	Doc													
9		Restoration	20 days	Fri 8/2/24	Thu 8/29/24		C&M													
10		1000 Dublin	10 days	Mon 7/29/24	Fri 8/9/24															
11		Sewer	12 days	Fri 7/26/24	Mon 8/12/24	8	Doc													
12		Restoration	20 days	Wed 8/14/24	Tue 9/10/24															
13		1000 Cambronne	81 days	Wed 8/14/24	Wed 12/4/24															
14		Sewer	7 days	Tue 8/13/24	Wed 8/21/24	11	Doc													
15		Restoration	30 days	Fri 8/23/24	Thu 10/3/24		C&M													
16		Lining	10 days	Wed 1/1/25	Tue 1/14/25		BLD													
17		8100 Maple	65 days	Fri 8/23/24	Thu 11/21/24															
18		Sewer	8 days	Thu 8/22/24	Mon 9/2/24	14	Doc													
19		Restoration	30 days	Mon 9/16/24	Fri 10/25/24		C&M													
20		Lining	10 days	Wed 1/1/25	Tue 1/14/25		BLD													
21		1600 Dublin	60 days	Mon 6/24/24	Fri 9/13/24															
22		Sewer	12 days	Mon 6/24/24	Tue 7/9/24		Josh													
23		Restoration	30 days	Tue 7/23/24	Mon 9/2/24		C&M													
24		8200 Green	46 days	Wed 7/10/24	Wed 9/11/24															
25		Sewer	12 days	Wed 7/10/24	Thu 7/25/24	22	Josh													
26		Restoration	30 days	Thu 8/1/24	Wed 9/11/24		C&M													
27		8200 Birch	26 days	Mon 7/29/24	Mon 9/2/24															
28		Sewer	12 days	Fri 7/26/24	Mon 8/12/24	25	Josh													
29		Restoration	30 days	Tue 8/27/24	Mon 10/7/24		C&M													
30		8200 Hickory	89 days	Wed 8/14/24	Mon 12/16/24															
31		Sewer	12 days	Tue 8/13/24	Wed 8/28/24	28	Josh													
32		Restoration	30 days	Mon 9/9/24	Fri 10/18/24		C&M													
33		8300 Hickory	38 days	Fri 8/30/24	Tue 10/22/24															
34		Sewer	12 days	Thu 8/29/24	Fri 9/13/24	31	Josh													
35		Restoration	30 days	Mon 9/30/24	Fri 11/8/24		C&M													
36		8400 Hickory	66 days	Tue 9/17/24	Tue 12/17/24															
37		Sewer	12 days	Mon 9/16/24	Tue 10/1/24	34	Josh													
38		Restoration	30 days	Wed 10/16/24	Tue 11/26/24		C&M													
39		1900 Monroe	127 days	Thu 6/27/24	Fri 12/20/24															
40		Sewer	10 days	Thu 6/27/24	Wed 7/10/24		John													

Project: SWB 30257 Project Sched
Date: Wed 6/19/24


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr '24				May '24				Jun '24				
								10	17	24	31	7	14	21	28	5	12	19	26	2
41		Restoration	30 days	Wed 7/24/24	Tue 9/3/24		C&M													
42		Lining	10 days	Wed 1/1/25	Tue 1/14/25		BLD													
43		8800 Spruce	62 days	Thu 7/11/24	Fri 10/4/24															
44		Sewer	10 days	Thu 7/11/24	Wed 7/24/24	40	John													
45		Restoration	30 days	Mon 8/5/24	Fri 9/13/24		C&M													
46		Lining	10 days	Wed 1/1/25	Tue 1/14/25		BLD													
47		1900 General Ogden	62 days	Thu 7/25/24	Fri 10/18/24															
48		Sewer	10 days	Thu 7/25/24	Wed 8/7/24	44	John													
49		Restoration	30 days	Mon 8/19/24	Fri 9/27/24		C&M													
50		Lining	10 days	Wed 1/1/25	Tue 1/14/25		BLD													
51		9000 Cohn	62 days	Thu 8/8/24	Fri 11/1/24															
52		Sewer	5 days	Thu 8/8/24	Wed 8/14/24	48	John													
53		Restoration	20 days	Wed 8/28/24	Tue 9/24/24		C&M													
54		Lining	10 days	Wed 1/1/25	Tue 1/14/25		BLD													
55		1800 Hollygrove	62 days	Thu 8/15/24	Fri 11/8/24															
56		Sewer	12 days	Thu 8/15/24	Fri 8/30/24	52	John													
57		Restoration	30 days	Mon 9/16/24	Fri 10/25/24		C&M													
58		1800 General Ogden	62 days	Mon 9/2/24	Tue 11/26/24															
59		Sewer	10 days	Mon 9/2/24	Fri 9/13/24	56	John													
60		Restoration	30 days	Fri 9/27/24	Thu 11/7/24		C&M													
61		1800 General Ogden (Leonidas)	62 days	Fri 9/13/24	Mon 12/9/24															
62		Sewer	10 days	Mon 9/16/24	Fri 9/27/24	59	John													
63		Restoration	30 days	Mon 10/7/24	Fri 11/15/24		C&M													
64		8800 Hickory	62 days	Mon 9/30/24	Tue 12/24/24															
65		Sewer	10 days	Mon 9/30/24	Fri 10/11/24	62	John													
66		Restoration	30 days	Fri 10/25/24	Thu 12/5/24		C&M													
67		1400 Cambronne	62 days	Wed 9/4/24	Thu 11/28/24															
68		Sewer	12 days	Tue 9/3/24	Wed 9/18/24	18	Doc													
69		Restoration	30 days	Thu 10/3/24	Wed 11/13/24		C&M													
70		8400 Jeanette	62 days	Fri 9/20/24	Mon 12/16/24															
71		Sewer	10 days	Thu 9/19/24	Wed 10/2/24	68	Doc													
72		Restoration	30 days	Thu 10/17/24	Wed 11/27/24		C&M													
73		1400 Leonidas	62 days	Mon 10/7/24	Tue 12/31/24															
74		Sewer	10 days	Thu 10/3/24	Wed 10/16/24	71	Doc													
75		Restoration	30 days	Thu 10/31/24	Wed 12/11/24		C&M													
76		8700 Jeanette	62 days	Mon 10/21/24	Tue 1/14/25															
77		Sewer	10 days	Thu 10/17/24	Wed 10/30/24	74	Doc													
78		Restoration	30 days	Mon 11/18/24	Fri 12/27/24		C&M													
79		1800 Leonidas (PR)	62 days	Thu 10/3/24	Fri 12/27/24															
80		Sewer	10 days	Wed 10/2/24	Tue 10/15/24	37	Josh													

Project: SWB 30257 Project Sched Date: Wed 6/19/24	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Apr '24				May '24				Jun '24						
								10	17	24	31	7	14	21	28	5	12	19	26	2	9	16
81		Restoration	30 days	Wed 10/30/24	Tue 12/10/24		C&M															
82		Lining	10 days	Wed 1/1/25	Tue 1/14/25		BLD															
83		1800 Leonidas (SM)	62 days	Thu 10/17/24	Fri 1/10/25																	
84		Sewer	10 days	Wed 10/16/24	Tue 10/29/24	80	Josh															
85		Restoration	30 days	Fri 11/15/24	Thu 12/26/24		C&M															
86		8700 Hickory	62 days	Mon 10/14/24	Tue 1/7/25																	
87		Sewer	10 days	Mon 10/14/24	Fri 10/25/24	65	John															
88		Restoration	30 days	Mon 11/11/24	Fri 12/20/24		C&M															
89		8600 Hickory	62 days	Mon 10/21/24	Tue 1/14/25																	
90		Sewer	10 days	Mon 10/28/24	Fri 11/8/24	87	John															
91		Restoration	30 days	Fri 11/22/24	Thu 1/2/25		C&M															
92		8500 Hickory	62 days	Mon 11/11/24	Tue 2/4/25																	
93		Sewer	10 days	Wed 10/30/24	Tue 11/12/24	84	Josh															
94		Restoration	30 days	Thu 12/5/24	Wed 1/15/25		C&M															
95		1500 General Ogden	10 days	Mon 8/12/24	Fri 8/23/24																	
96		Lining	10 days	Mon 8/12/24	Fri 8/23/24		BLD															
97		2000 Monroe Ct	10 days	Mon 8/12/24	Fri 8/23/24																	
98		Lining	10 days	Mon 8/12/24	Fri 8/23/24		BLD															
99		8800 Cohn	10 days	Mon 8/12/24	Fri 8/23/24																	
100		Lining	10 days	Mon 8/12/24	Fri 8/23/24		BLD															
101		Manhole Rehabilitation	25 days	Sun 12/1/24	Thu 1/2/25																	
102		First Mobilization	25 days	Sun 12/1/24	Thu 1/2/25		Python															
103		Consent Decree 25%		Sat 8/31/24																		
104		Consent Decree 50%		Fri 11/22/24																		
105		Consent Decree 75%		Thu 2/13/25																		

Project: SWB 30257 Project Sched Date: Wed 6/19/24	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only			
	Summary		Inactive Task		Duration-only		Finish-only			

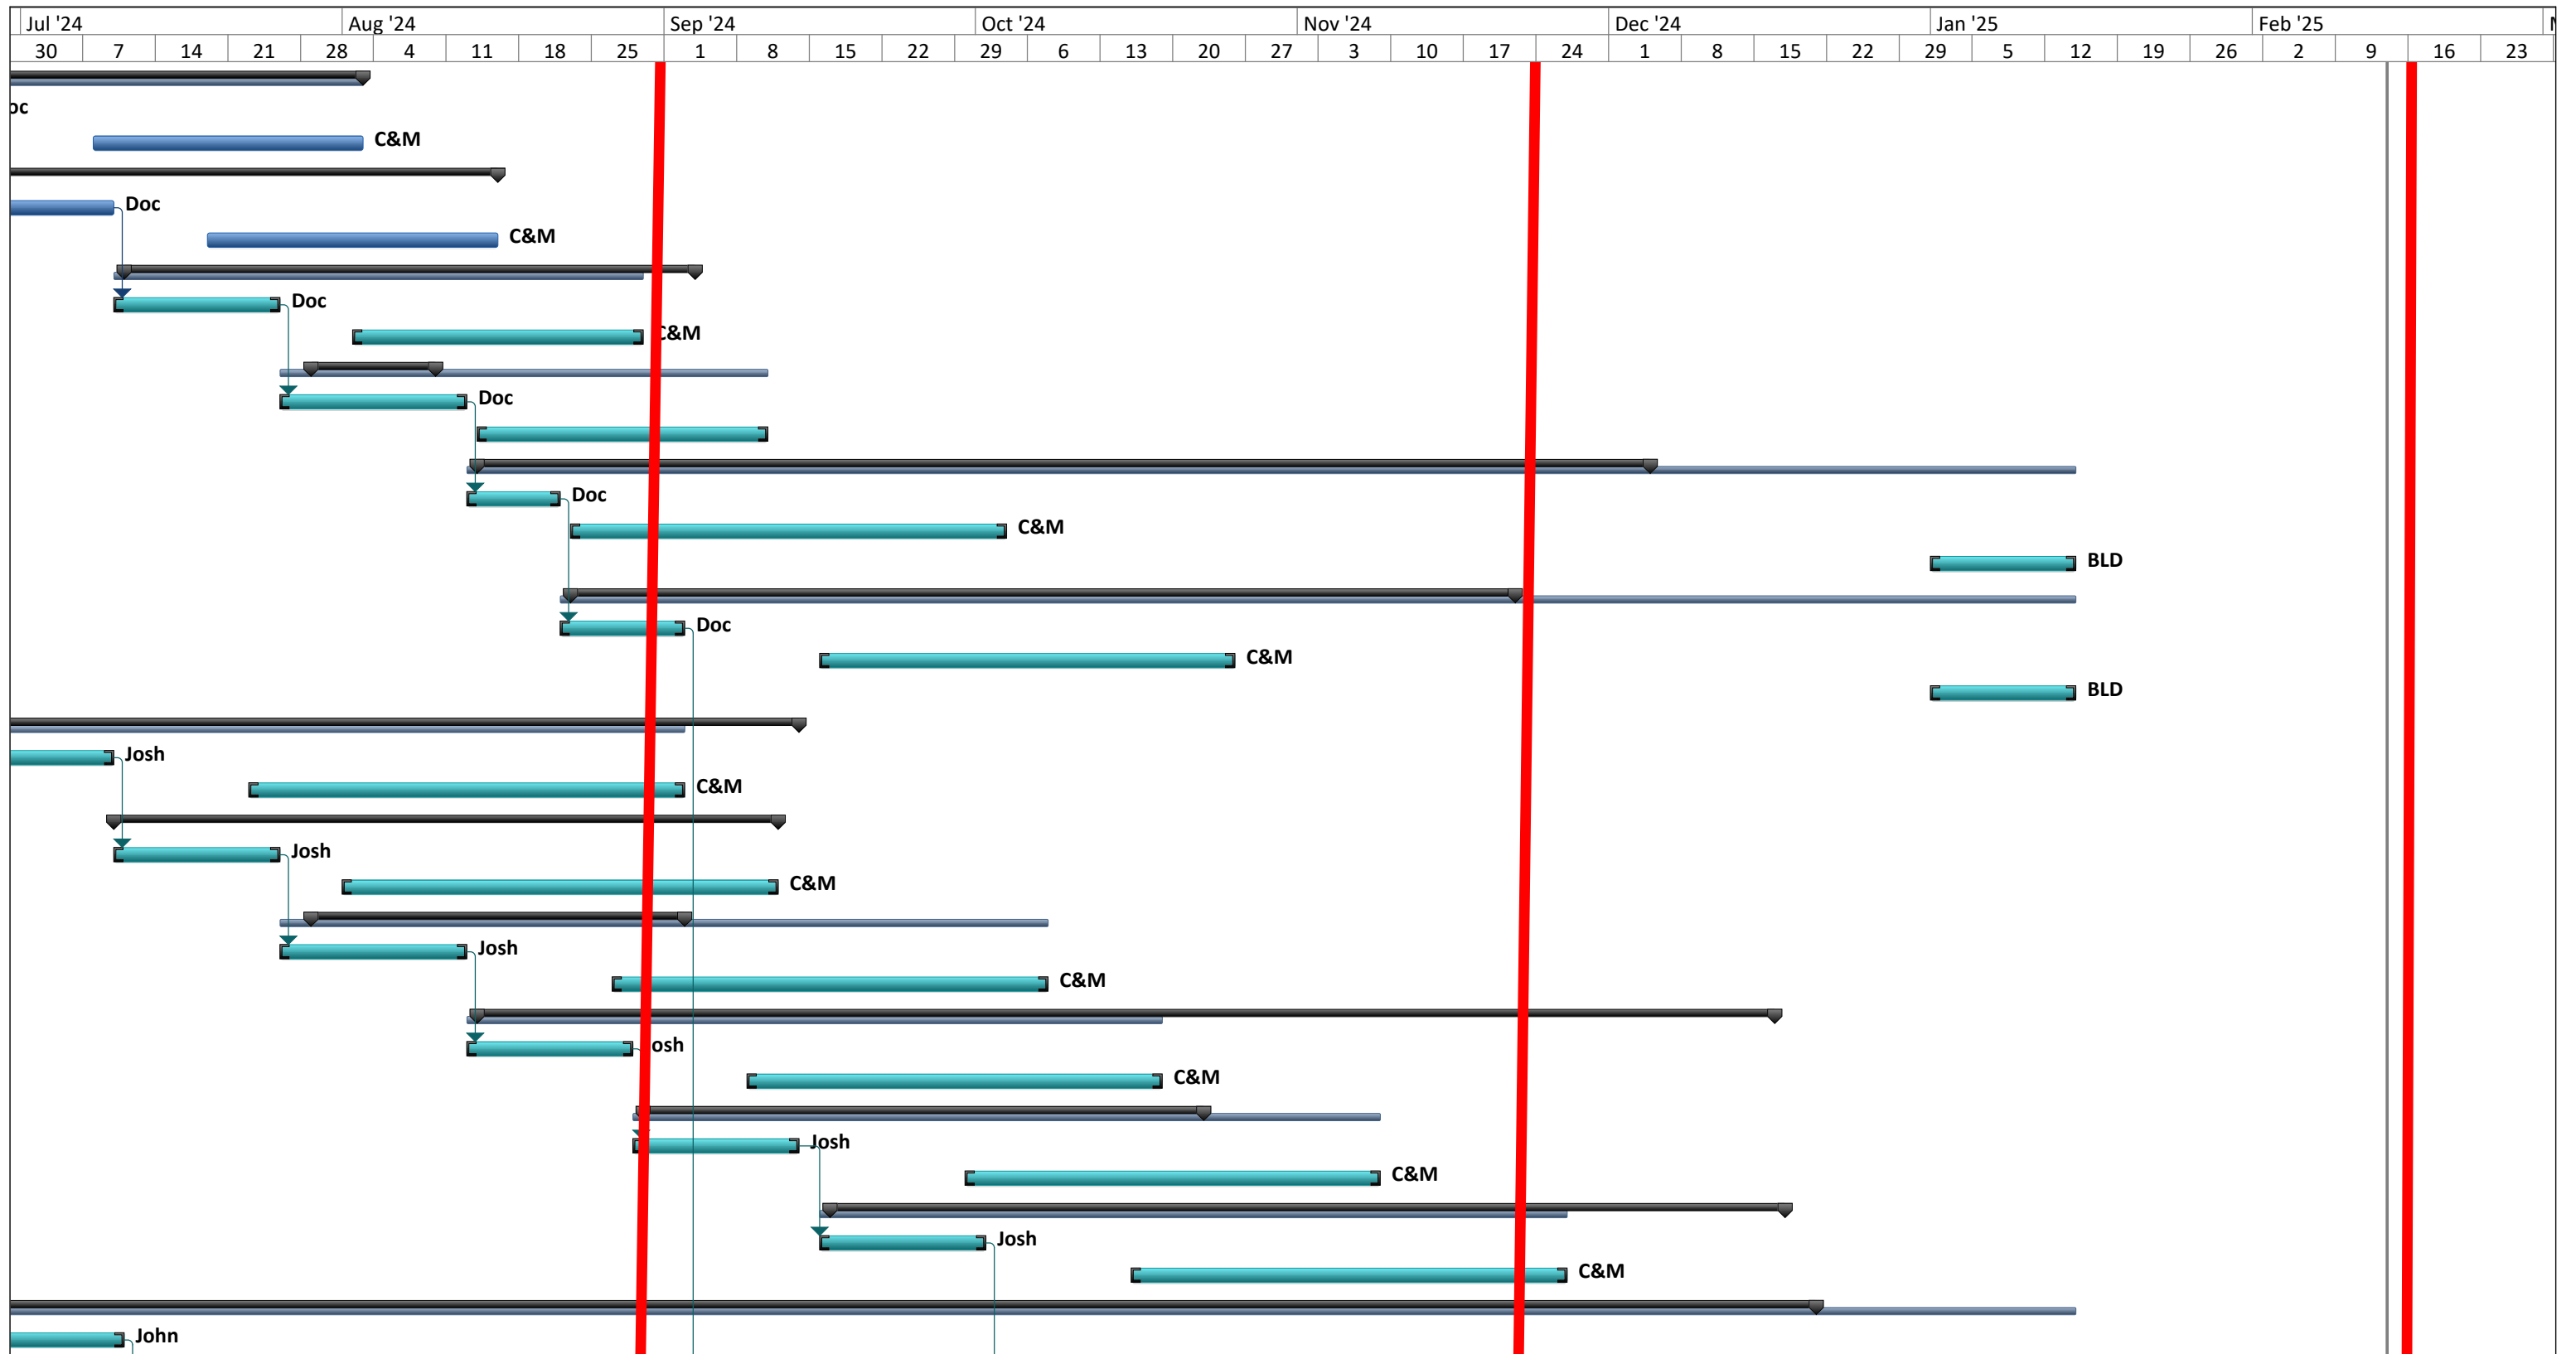


Project: SWB 30257 Project Sched
Date: Wed 6/19/24

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

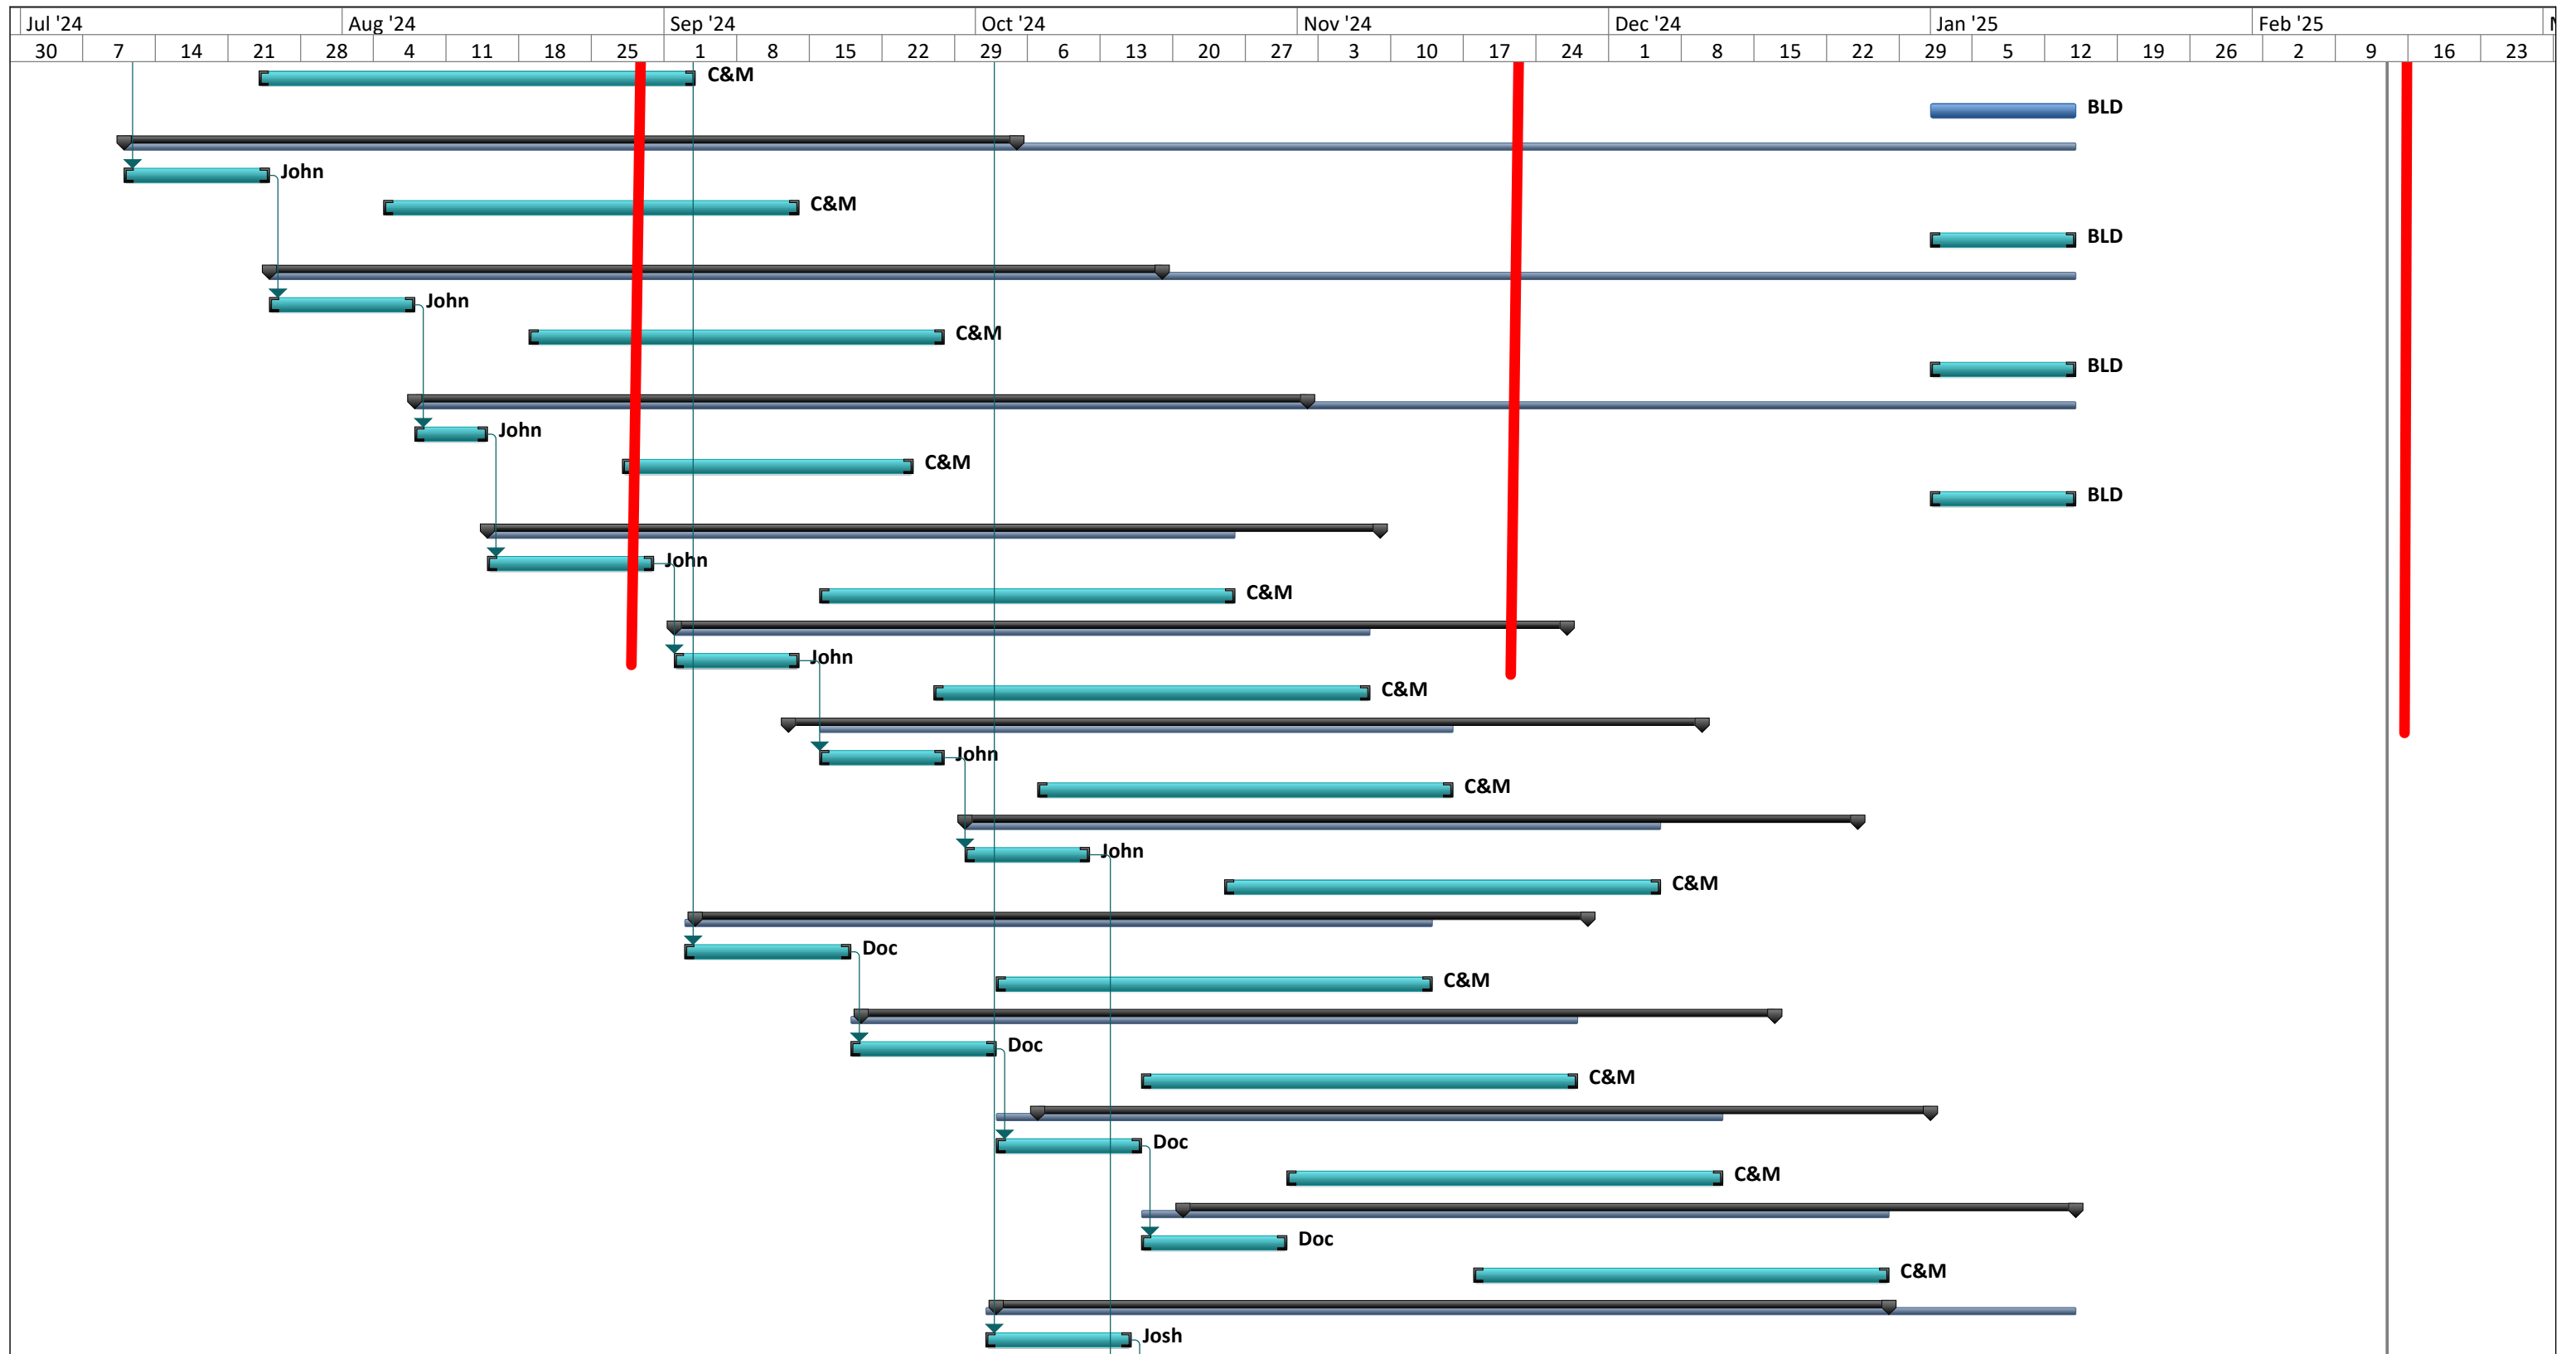

Project: SWB 30257 Project Sched
 Date: Wed 6/19/24

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

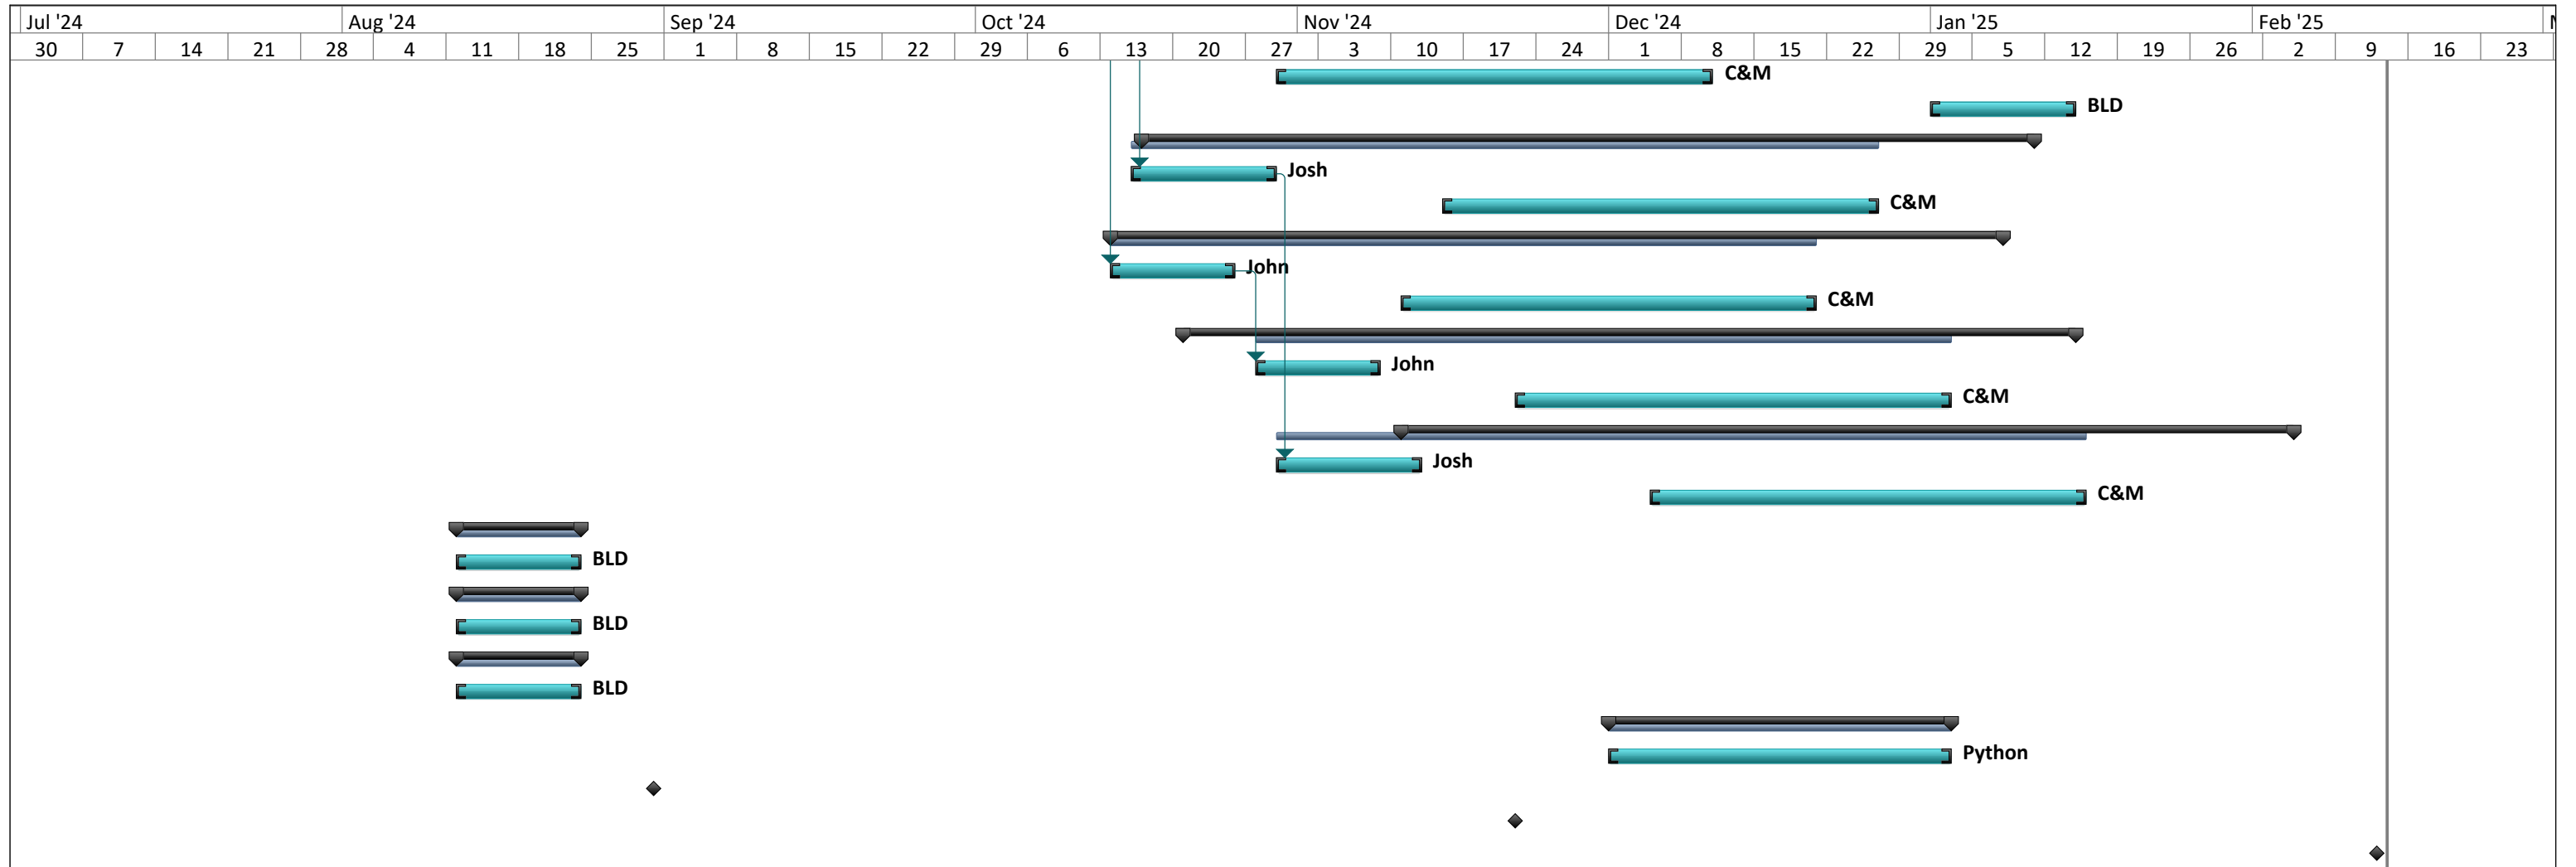

Project: SWB 30257 Project Sched
Date: Wed 6/19/24

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			
