ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
39						
40		**Sewer Rehabilitation**				
41						
42		**2400 Dante**	**9 days**	**Mon 8/5/24**	**Thu 8/15/24**	
43		CCTV and Lateral Launch	2 days	Mon 8/5/24	Tue 8/6/24	
44		Mainline and Service Repairs	4 days	Mon 8/12/24	Thu 8/15/24	
45						
46		**Roadway Restoration**				
47						
48		**8500 Nelson**	**5 days?**	**Mon 8/5/24**	**Fri 8/9/24**	
49		Install and Grade Base Course	3 days	Mon 8/5/24	Wed 8/7/24	
50		ADA Ramps and S/W	2 days	Thu 8/8/24	Fri 8/9/24	49
51			1 day?	Mon 8/5/24	Mon 8/5/24	
52		**8400 Nelson**	**7 days**	**Mon 8/12/24**	**Tue 8/20/24**	
53		Install and Grade Base Course	5 days	Mon 8/12/24	Fri 8/16/24	50
54		ADA Ramps and S/w	2 days	Mon 8/19/24	Tue 8/20/24	53
55						
56		**30259 Carrollton Basin No 18**				
57						
58		**Two Week Look Ahead**	10 days	Mon 8/5/24	Fri 8/16/24	
59						
60		**Sewer Rehabilitation**				
61						
62		**3800 Mistletoe**	**10 days**	**Mon 8/5/24**	**Fri 8/16/24**	
63		Sewer Main Installation	2 days	Mon 8/5/24	Tue 8/6/24	
64		Sewer House Connections	5 days	Wed 8/7/24	Tue 8/13/24	63
65						
66		**4200 Eagle**	**1 day**	**Mon 8/5/24**	**Mon 8/5/24**	
67		Sewer House Connections	1 day	Mon 8/5/24	Mon 8/5/24	
68						
69		**3800 Leonidas**	**5 days**	**Mon 8/5/24**	**Fri 8/9/24**	
70		Mainline and Service Repairs	5 days	Mon 8/5/24	Fri 8/9/24	
71						
72		**3400 Clara (116-058/116-050)**	**2 days**	**Wed 8/14/24**	**Thu 8/15/24**	
73		Mainline Service Point Repair	1 day	Wed 8/14/24	Wed 8/14/24	
74		SHC	1 day	Thu 8/15/24	Thu 8/15/24	73
75						
76		**1000 Broadway**	**1 day**	**Thu 8/8/24**	**Thu 8/8/24**	

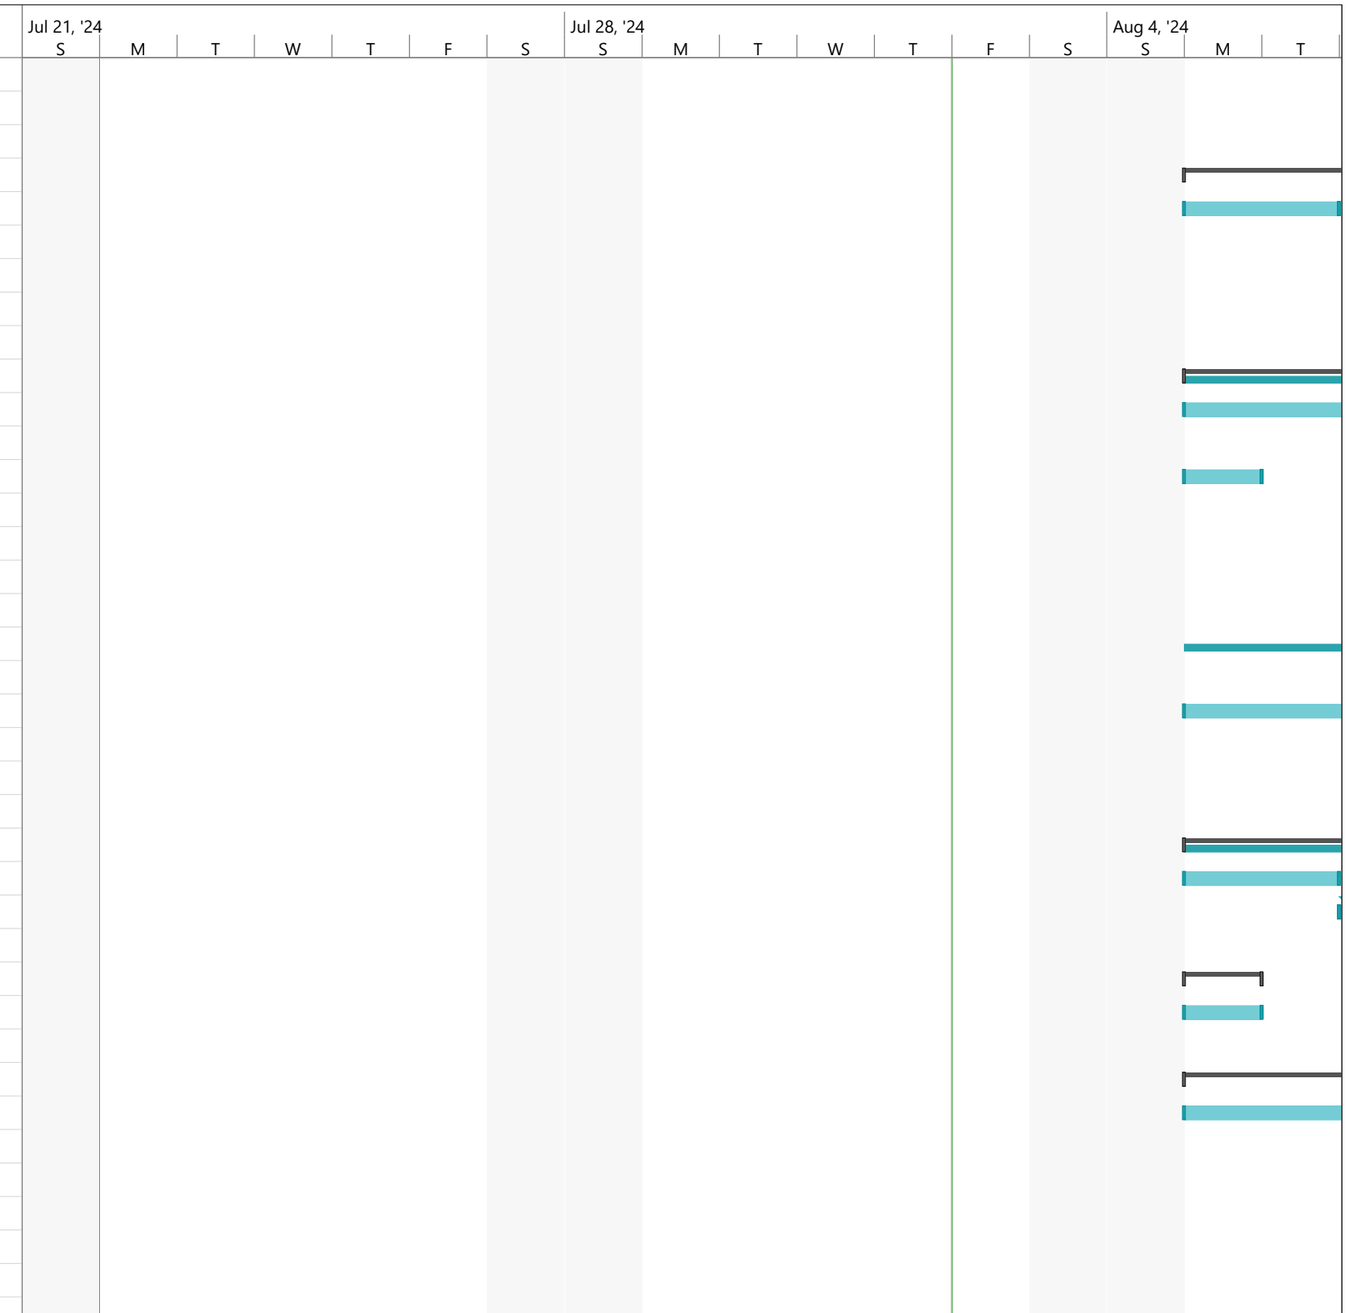

Project: 30256 Two Week Look
Date: Fri 8/2/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
77		Pre CCTV	1 day	Thu 8/8/24	Thu 8/8/24	
78						
79		**1100 Broadway**	**19 days**	**Mon 8/12/24**	**Thu 9/5/24**	
80		Mainline Point Repairs	8 days	Mon 8/12/24	Wed 8/21/24	
81		Post CCTV	1 day	Thu 8/22/24	Thu 8/22/24	80
82		Roadway Restoration	5 days	Fri 8/23/24	Thu 8/29/24	81
83						
84		**1200 Broadway**	**14 days**	**Mon 8/12/24**	**Thu 8/29/24**	
85		Mainline Point Repairs	8 days	Mon 8/12/24	Wed 8/21/24	
86		Post CCTV	1 day	Thu 8/22/24	Thu 8/22/24	85
87		Roadway Restoration	5 days	Fri 8/23/24	Thu 8/29/24	86
88						
89		**9100 Dixon**	**10 days**	**Mon 8/5/24**	**Fri 8/16/24**	
90		Mainline and Service Point Repairs	10 days	Mon 8/5/24	Fri 8/16/24	
91						
92		**30260 Carrollton Basin No. 19**				
93						
94		**Two Week Look Ahead**	10 days	Mon 8/5/24	Fri 8/16/24	
95						
96		**1900 Eagle St**	**10 days**	**Mon 8/5/24**	**Fri 8/16/24**	
97		Excavation of Pits	3 days	Mon 8/5/24	Wed 8/7/24	
98		Jack and Bore	1 day	Thu 8/8/24	Thu 8/8/24	97
99		Build SMHs	6 days	Fri 8/9/24	Fri 8/16/24	98
100		Sewer Main Installation	6 days	Fri 8/9/24	Fri 8/16/24	98
101		6" Sewer Main Installation	6 days	Fri 8/9/24	Fri 8/16/24	98
102						
103		**30261 Carrolton Basin No. 20**	17 days	Mon 8/5/24	Tue 8/27/24	
104						
105		**Two Week Look Ahead**	10 days	Mon 8/5/24	Fri 8/16/24	
106						
107		**CCTV**	**12 days**	**Mon 8/12/24**	**Tue 8/27/24**	
108						
109		**8700 Olive St**	**12 days**	**Mon 8/12/24**	**Tue 8/27/24**	
110		Pre CCTV	1 day	Mon 8/12/24	Mon 8/12/24	
111		Lateral Launch	1 day	Tue 8/27/24	Tue 8/27/24	114
112		**1400 Dante St**	**10 days**	**Tue 8/13/24**	**Mon 8/26/24**	
113		Pre CCTV	1 day	Tue 8/13/24	Tue 8/13/24	110

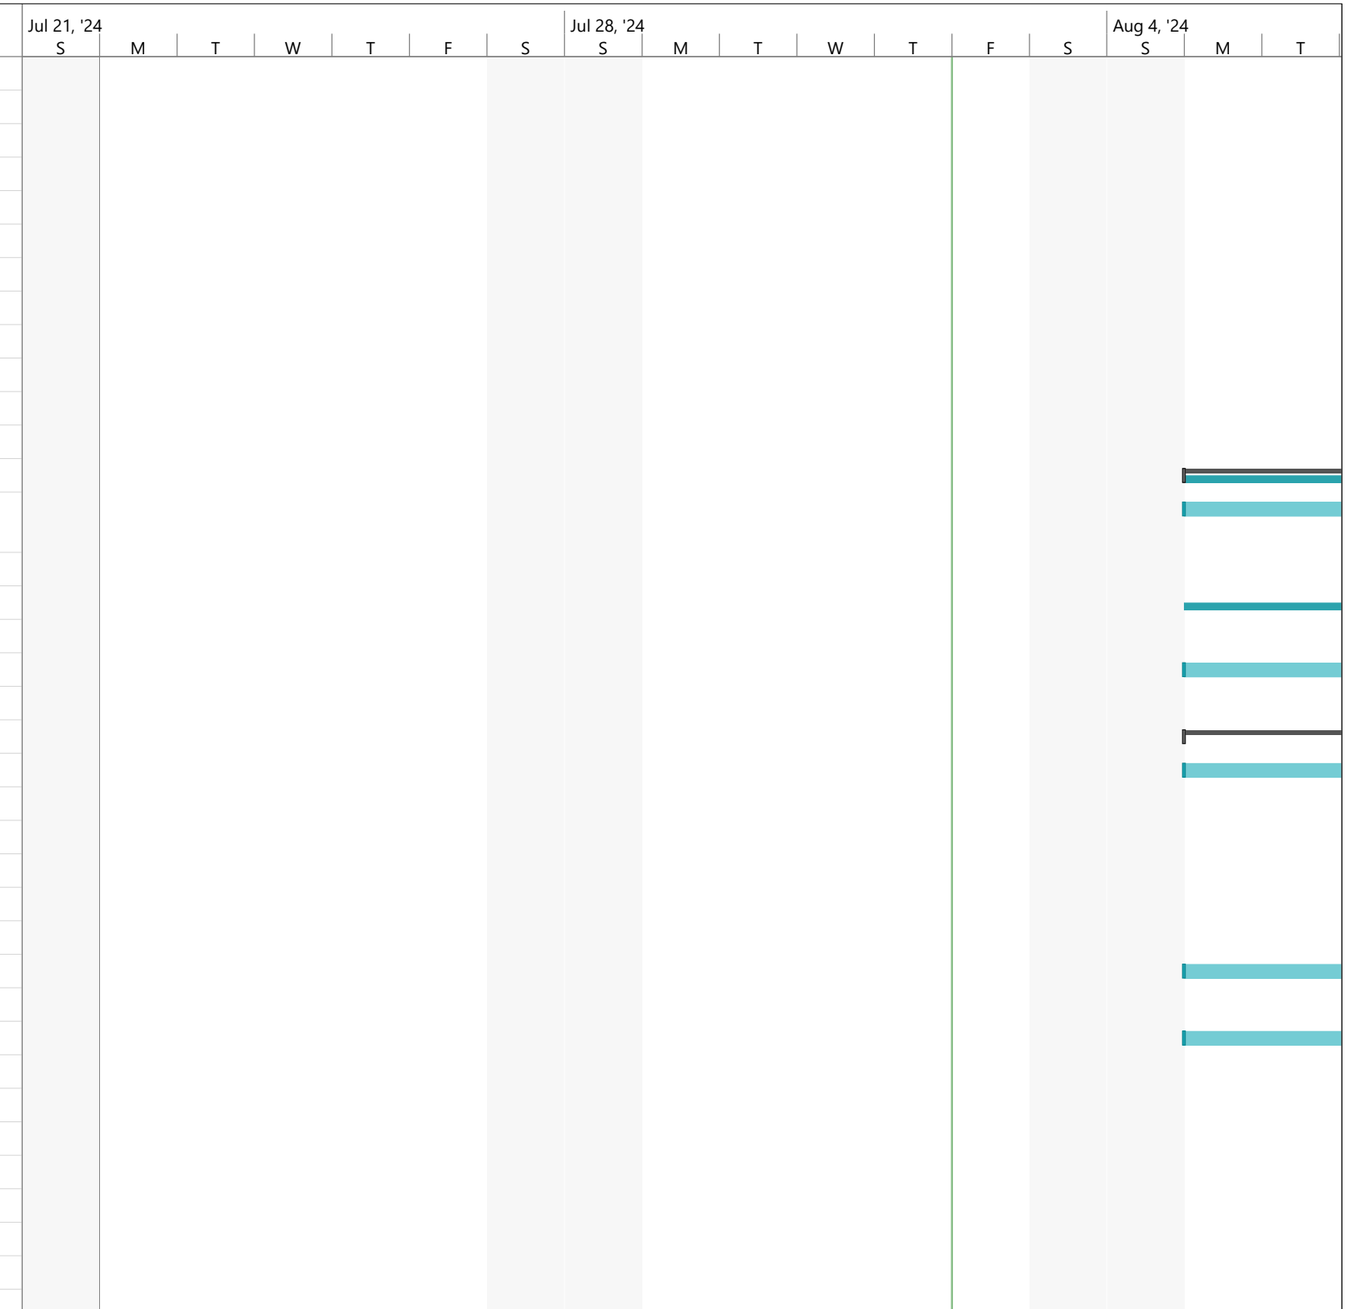

Project: 30256 Two Week Look
Date: Fri 8/2/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
