ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1		**30261 Carrolton Basin No. 20**	10 days	Mon 9/9/24	Fri 9/20/24		
2							
3		**Two Week Look Ahead**	10 days	Mon 9/9/24	Fri 9/20/24		
4							
5		**CCTV**	**14 days**	**Mon 9/9/24**	**Thu 9/26/24**		
6							
7		**8700 Olive St**	**10 days**	**Mon 9/9/24**	**Fri 9/20/24**		
8		Pre CCTV	1 day	Thu 9/19/24	Thu 9/19/24	20	
9		Lateral Launch	1 day	Fri 9/20/24	Fri 9/20/24	8	
10		**1400 Dante St**	**2 days**	**Wed 9/11/24**	**Thu 9/12/24**		
11		Pre CCTV	1 day	Wed 9/11/24	Wed 9/11/24	17	
12		Lateral Launch	1 day	Thu 9/12/24	Thu 9/12/24	11	
13		**1900 Dante St**	**2 days**	**Fri 9/13/24**	**Mon 9/16/24**		
14		Pre CCTV	1 day	Fri 9/13/24	Fri 9/13/24	12	
15		Lateral Launch	1 day	Mon 9/16/24	Mon 9/16/24	14	
16		**8300 Apple St**	**1 day**	**Tue 9/10/24**	**Tue 9/10/24**		
17		Lateral Launch	1 day	Tue 9/10/24	Tue 9/10/24	22	
18		**9100 Olive St**	**2 days**	**Tue 9/17/24**	**Wed 9/18/24**		
19		Pre CCTV	1 day	Tue 9/17/24	Tue 9/17/24	15	
20		Lateral Launch	1 day	Wed 9/18/24	Wed 9/18/24	19	
21		**8500 Apple St**	**1 day**	**Mon 9/9/24**	**Mon 9/9/24**		
22		Lateral Launch	1 day	Mon 9/9/24	Mon 9/9/24		

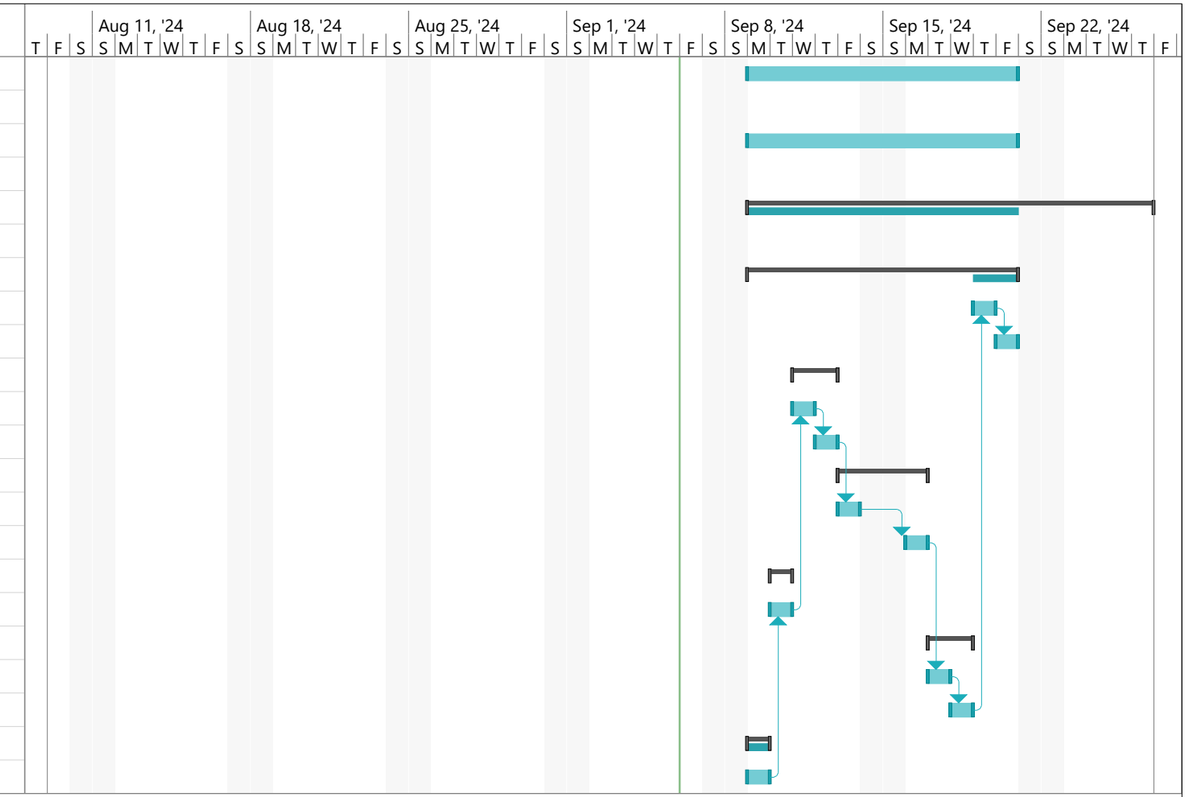

Project: 30261 Two Week Look
Date: Fri 9/6/24

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
