ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**30256 Carrollton Basin No.15**				
2						
3		**Two Week Look Ahead**	9 days	Tue 8/27/24	Fri 9/6/24	
4						
5		**CCTV**				
6						
7		**8300 Oleander**	**1 day**	**Fri 8/30/24**	**Fri 8/30/24**	
8		Post CCTV	1 day	Fri 8/30/24	Fri 8/30/24	
9						
10		**2900 Joliet**	**1 day**	**Fri 8/30/24**	**Fri 8/30/24**	
11		Lateral Launch	1 day	Fri 8/30/24	Fri 8/30/24	
12						
13		**8300 Palmetto**	**2 days**	**Fri 8/30/24**	**Mon 9/2/24**	
14		CCTV	1 day	Fri 8/30/24	Fri 8/30/24	
15		Lateral Launch	1 day	Fri 8/30/24	Fri 8/30/24	
16						
17		**CIPP**				
18						
19		**8500 Pritchard**	**1 day**	**Tue 8/27/24**	**Tue 8/27/24**	
20		CIPP	1 day	Tue 8/27/24	Tue 8/27/24	
21						
22		**3100 Cambronne**	**1 day**	**Wed 8/28/24**	**Wed 8/28/24**	
23		CIPP	1 day	Wed 8/28/24	Wed 8/28/24	
24						
25		**8300 Fig**	**1 day**	**Thu 8/29/24**	**Thu 8/29/24**	
26		CIPP	1 day	Thu 8/29/24	Thu 8/29/24	
27						
28		**Roadway Restoration**				
29						
30		**Pritchard and Cambronne**	**3 days**	**Wed 8/28/24**	**Fri 8/30/24**	
31		Form Up Intersection	2 days	Wed 8/28/24	Thu 8/29/24	
32		Pour 8" Concrete	1 day	Fri 8/30/24	Fri 8/30/24	
33		**3500 Dante**	**13 days**	**Tue 8/27/24**	**Thu 9/12/24**	
34		Remove and Install Base Course	5 days	Tue 8/27/24	Mon 9/2/24	
35		Frame Curb and Gutter	2 days	Tue 9/3/24	Wed 9/4/24	34
36		Frame S/W and D/W	3 days	Thu 9/5/24	Mon 9/9/24	35
37		**8500 Apricot**	**3 days**	**Fri 8/30/24**	**Tue 9/3/24**	
38		Asphalt Patches	1 day	Fri 8/30/24	Fri 8/30/24	

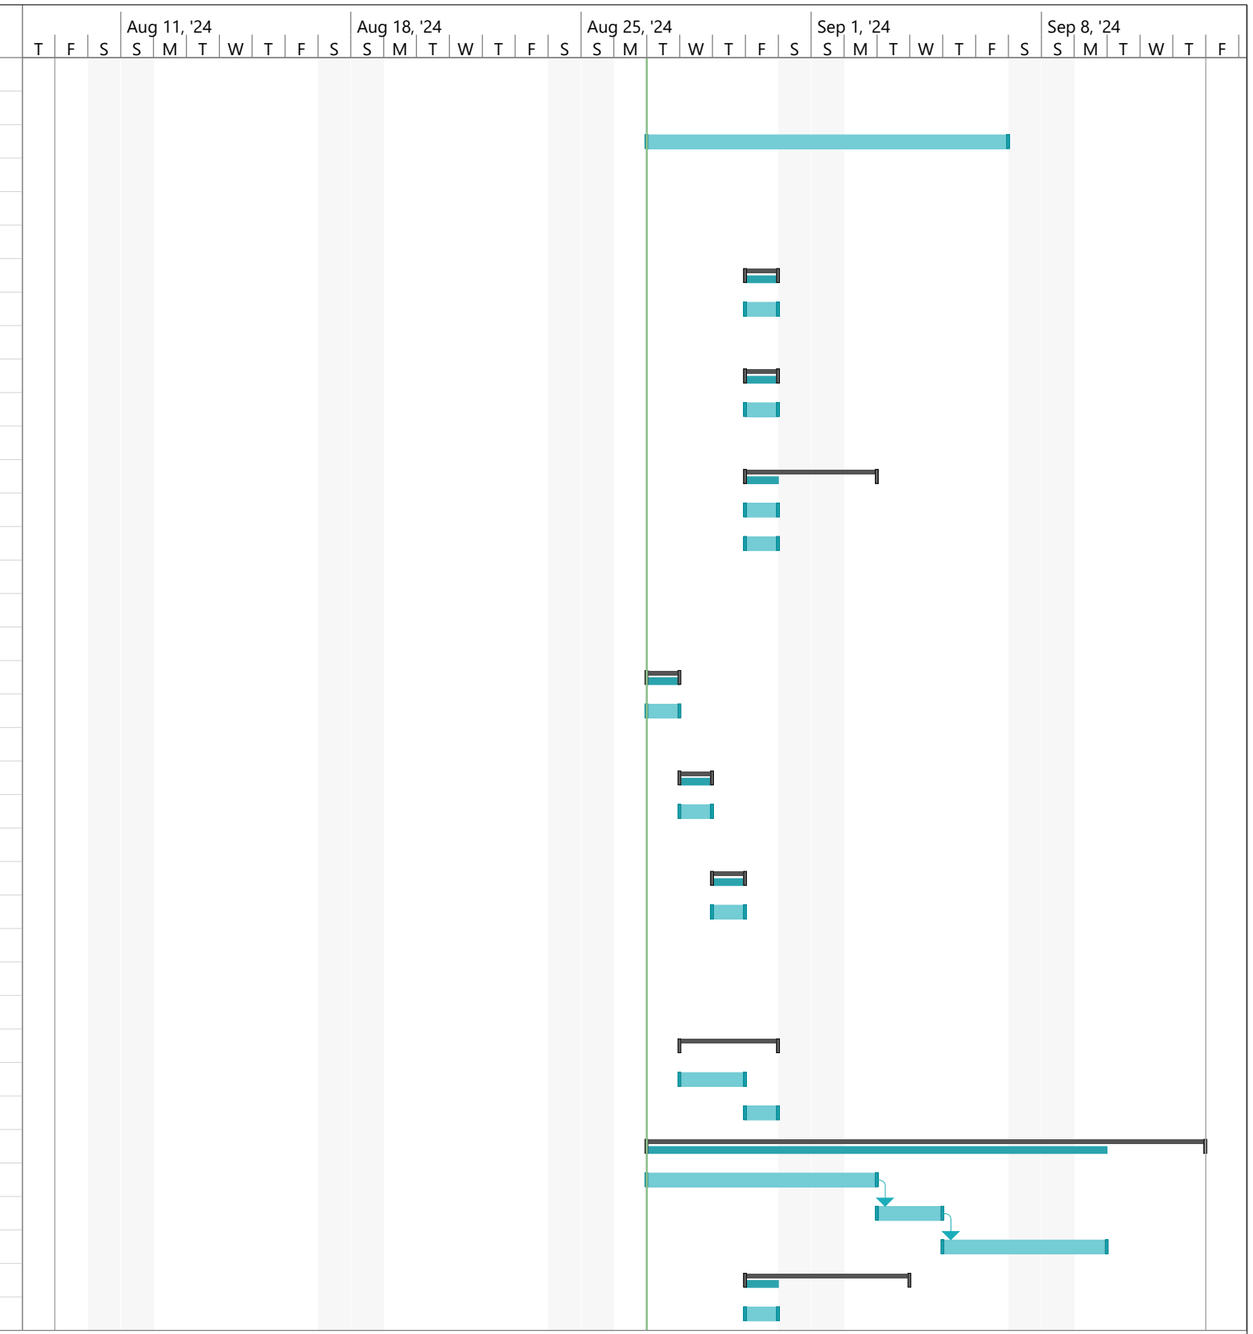

Project: 30256 Two Week Look
Date: Tue 8/27/24

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
39		**3200 Dante**	**1 day**	**Fri 8/30/24**	**Fri 8/30/24**	
40		Finish Asphalt	1 day	Fri 8/30/24	Fri 8/30/24	



Project: 30256 Two Week Look
Date: Tue 8/27/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
