ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**30256 Carrollton Basin No.15**				
2						
3		**Two Week Look Ahead**	9 days	Tue 9/3/24	Fri 9/13/24	
4						
5		**CCTV**				
6						
7		**2900 Joliet**	**1 day**	**Wed 9/4/24**	**Wed 9/4/24**	
8		Lateral Launch	1 day	Wed 9/4/24	Wed 9/4/24	
9						
10		**8300 Palmetto**	**2 days**	**Fri 9/6/24**	**Mon 9/9/24**	
11		CCTV	1 day	Fri 9/6/24	Fri 9/6/24	
12		Lateral Launch	1 day	Fri 9/6/24	Fri 9/6/24	
13						
14		**300 Lowerline**	**1 day**	**Fri 9/6/24**	**Fri 9/6/24**	
15		Lateral Launch	1 day	Fri 9/6/24	Fri 9/6/24	
16						
17		**CIPP**				
18						
19		**3100 Cambronne**	**1 day**	**Mon 9/9/24**	**Mon 9/9/24**	
20		CIPP	1 day	Mon 9/9/24	Mon 9/9/24	
21						
22		**8300 Fig**	**1 day**	**Tue 9/10/24**	**Tue 9/10/24**	
23		CIPP	1 day	Tue 9/10/24	Tue 9/10/24	
24						
25		**Roadway Restoration**				
26						
27		**Pritchard and Cambronne**	**1 day**	**Wed 9/4/24**	**Wed 9/4/24**	
28		Pour 8" Concrete	1 day	Wed 9/4/24	Wed 9/4/24	
29		**3500 Dante**	**4 days**	**Tue 9/3/24**	**Fri 9/6/24**	
30		Remove and Install Base Course	2 days	Tue 9/3/24	Wed 9/4/24	
31		Frame Curb and Gutter	1 day	Thu 9/5/24	Thu 9/5/24	30
32		Frame S/W and D/W	1 day	Thu 9/5/24	Thu 9/5/24	30
33		**8500 Apricot**	**2 days**	**Tue 9/3/24**	**Wed 9/4/24**	
34		Asphalt Patches	1 day	Tue 9/3/24	Tue 9/3/24	
35		Frame Curb and Gutter	1 day	Tue 9/3/24	Tue 9/3/24	
36		Pour Curb and Gutter	1 day	Wed 9/4/24	Wed 9/4/24	
37		**3200 Dante**	**1 day**	**Tue 9/3/24**	**Tue 9/3/24**	
38		Finish Asphalt	1 day	Tue 9/3/24	Tue 9/3/24	

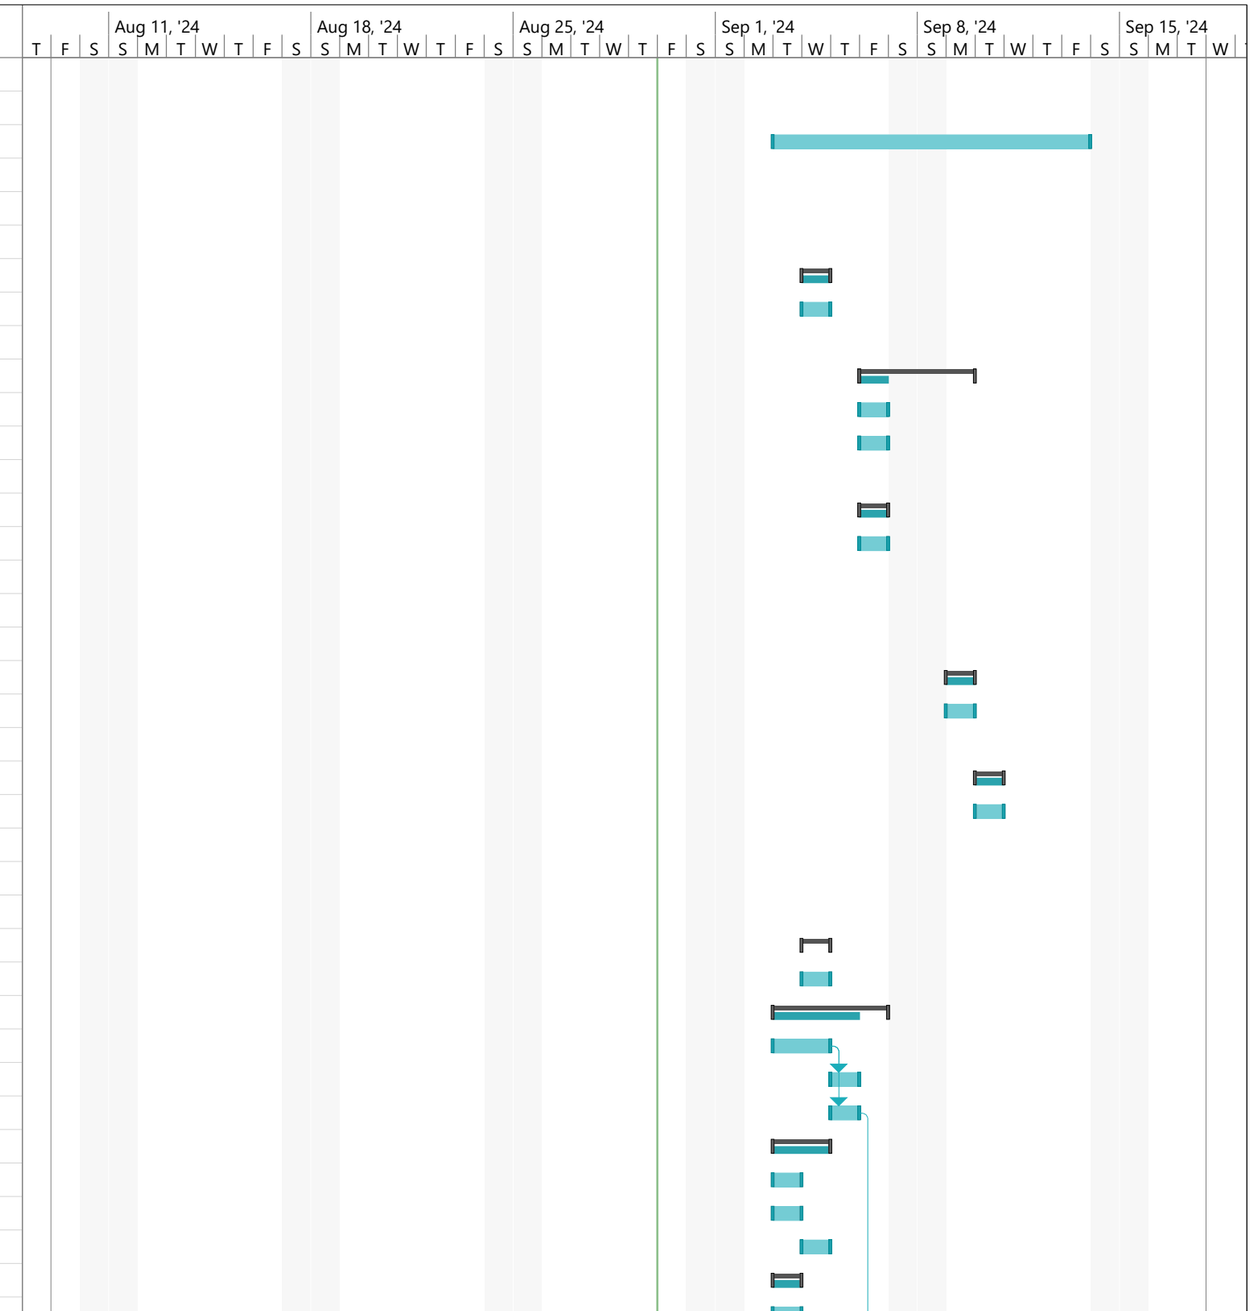

Project: 30256 Two Week Look
Date: Fri 8/30/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
39		**2600 Dublin**	**8 days**	**Fri 9/6/24**	**Tue 9/17/24**	
40		Remove and Install Base Course	5 days	Fri 9/6/24	Thu 9/12/24	32
41		Frame Curb and Gutter	1 day	Fri 9/13/24	Fri 9/13/24	40
42		Pour Curb and Gutter	1 day	Mon 9/16/24	Mon 9/16/24	41
43		Asphalt	1 day	Tue 9/17/24	Tue 9/17/24	42



Project: 30256 Two Week Look
Date: Fri 8/30/24

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
