ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
77		Pre CCTV	1 day	Thu 8/8/24	Thu 8/8/24	
78						
79		**1100 Broadway**	**19 days**	**Mon 8/12/24**	**Thu 9/5/24**	
80		Mainline Point Repairs	8 days	Mon 8/12/24	Wed 8/21/24	
81		Post CCTV	1 day	Thu 8/22/24	Thu 8/22/24	80
82		Roadway Restoration	5 days	Fri 8/23/24	Thu 8/29/24	81
83						
84		**1200 Broadway**	**14 days**	**Mon 8/12/24**	**Thu 8/29/24**	
85		Mainline Point Repairs	8 days	Mon 8/12/24	Wed 8/21/24	
86		Post CCTV	1 day	Thu 8/22/24	Thu 8/22/24	85
87		Roadway Restoration	5 days	Fri 8/23/24	Thu 8/29/24	86
88						
89		**9100 Dixon**	**10 days**	**Mon 8/5/24**	**Fri 8/16/24**	
90		Mainline and Service Point Repairs	10 days	Mon 8/5/24	Fri 8/16/24	
91						
92		**30260 Carrollton Basin No. 19**				
93						
94		**Two Week Look Ahead**	10 days	Mon 8/5/24	Fri 8/16/24	
95						
96		**1900 Eagle St**	**10 days**	**Mon 8/5/24**	**Fri 8/16/24**	
97		Excavation of Pits	3 days	Mon 8/5/24	Wed 8/7/24	
98		Jack and Bore	1 day	Thu 8/8/24	Thu 8/8/24	97
99		Build SMHs	6 days	Fri 8/9/24	Fri 8/16/24	98
100		Sewer Main Installation	6 days	Fri 8/9/24	Fri 8/16/24	98
101		6" Sewer Main Installation	6 days	Fri 8/9/24	Fri 8/16/24	98
102						
103		**30261 Carrolton Basin No. 20**	17 days	Mon 8/5/24	Tue 8/27/24	
104						
105		**Two Week Look Ahead**	10 days	Mon 8/5/24	Fri 8/16/24	
106						
107		**CCTV**	**12 days**	**Mon 8/12/24**	**Tue 8/27/24**	
108						
109		**8700 Olive St**	**12 days**	**Mon 8/12/24**	**Tue 8/27/24**	
110		Pre CCTV	1 day	Mon 8/12/24	Mon 8/12/24	
111		Lateral Launch	1 day	Tue 8/27/24	Tue 8/27/24	114
112		**1400 Dante St**	**10 days**	**Tue 8/13/24**	**Mon 8/26/24**	
113		Pre CCTV	1 day	Tue 8/13/24	Tue 8/13/24	110

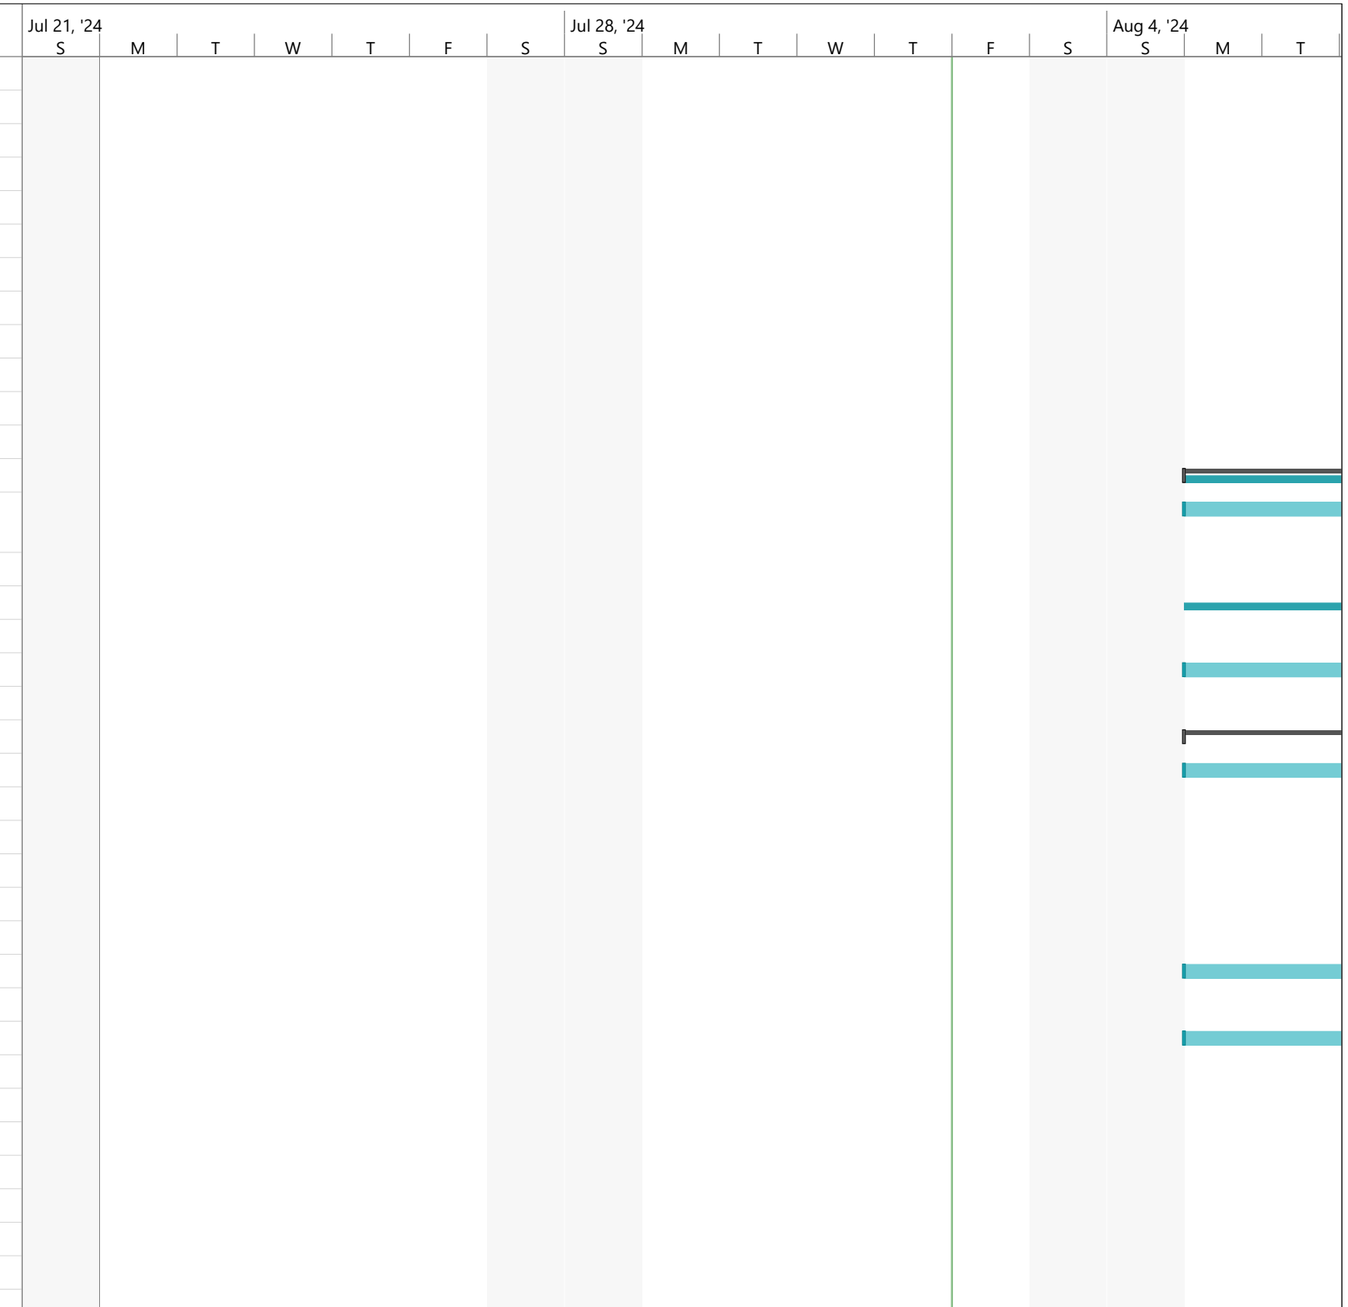

Project: 30256 Two Week Look
Date: Fri 8/2/24

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors
114			Lateral Launch	1 day	Mon 8/26/24	Mon 8/26/24	117
115			**1900 Dante St**	**8 days**	**Wed 8/14/24**	**Fri 8/23/24**	
116			Pre CCTV	1 day	Wed 8/14/24	Wed 8/14/24	113
117			Lateral Launch	1 day	Fri 8/23/24	Fri 8/23/24	120
118			**8300 Apple St**	**6 days**	**Thu 8/15/24**	**Thu 8/22/24**	
119			Pre CCTV	1 day	Thu 8/15/24	Thu 8/15/24	116
120			Lateral Launch	1 day	Thu 8/22/24	Thu 8/22/24	123
121			**9100 Olive St**	**4 days**	**Fri 8/16/24**	**Wed 8/21/24**	
122			Pre CCTV	1 day	Fri 8/16/24	Fri 8/16/24	119
123			Lateral Launch	1 day	Wed 8/21/24	Wed 8/21/24	126
124			**8500 Apple St**	**2 days**	**Mon 8/19/24**	**Tue 8/20/24**	
125			Pre CCTV	1 day	Mon 8/19/24	Mon 8/19/24	122
126			Lateral Launch	1 day	Tue 8/20/24	Tue 8/20/24	125

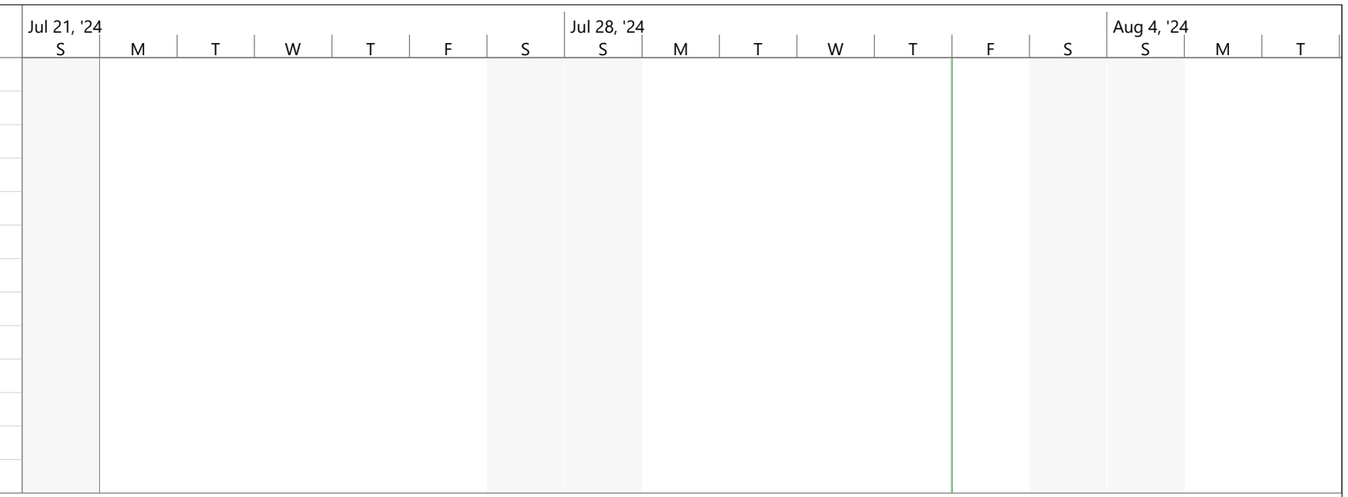

Project: 30256 Two Week Look
Date: Fri 8/2/24

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
