ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1			**30261 Carrolton Basin No. 20**	12 days	Mon 8/19/24	Tue 9/3/24		
2								
3			**Two Week Look Ahead**	10 days	Mon 8/19/24	Fri 8/30/24		
4								
5			**CCTV**	**12 days**	**Mon 8/19/24**	**Tue 9/3/24**		
6								
7			**8700 Olive St**	**12 days**	**Mon 8/19/24**	**Tue 9/3/24**		
8			Pre CCTV	1 day	Mon 8/19/24	Mon 8/19/24		
9			Lateral Launch	1 day	Tue 9/3/24	Tue 9/3/24	12	
10			**1400 Dante St**	**10 days**	**Tue 8/20/24**	**Mon 9/2/24**		
11			Pre CCTV	1 day	Tue 8/20/24	Tue 8/20/24	8	
12			Lateral Launch	1 day	Mon 9/2/24	Mon 9/2/24	15	
13			**1900 Dante St**	**8 days**	**Wed 8/21/24**	**Fri 8/30/24**		
14			Pre CCTV	1 day	Wed 8/21/24	Wed 8/21/24	11	
15			Lateral Launch	1 day	Fri 8/30/24	Fri 8/30/24	18	
16			**8300 Apple St**	**6 days**	**Thu 8/22/24**	**Thu 8/29/24**		
17			Pre CCTV	1 day	Thu 8/22/24	Thu 8/22/24	14	
18			Lateral Launch	1 day	Thu 8/29/24	Thu 8/29/24	21	
19			**9100 Olive St**	**4 days**	**Fri 8/23/24**	**Wed 8/28/24**		
20			Pre CCTV	1 day	Fri 8/23/24	Fri 8/23/24	17	
21			Lateral Launch	1 day	Wed 8/28/24	Wed 8/28/24	24	
22			**8500 Apple St**	**2 days**	**Mon 8/26/24**	**Tue 8/27/24**		
23			Pre CCTV	1 day	Mon 8/26/24	Mon 8/26/24	20	
24			Lateral Launch	1 day	Tue 8/27/24	Tue 8/27/24	23	

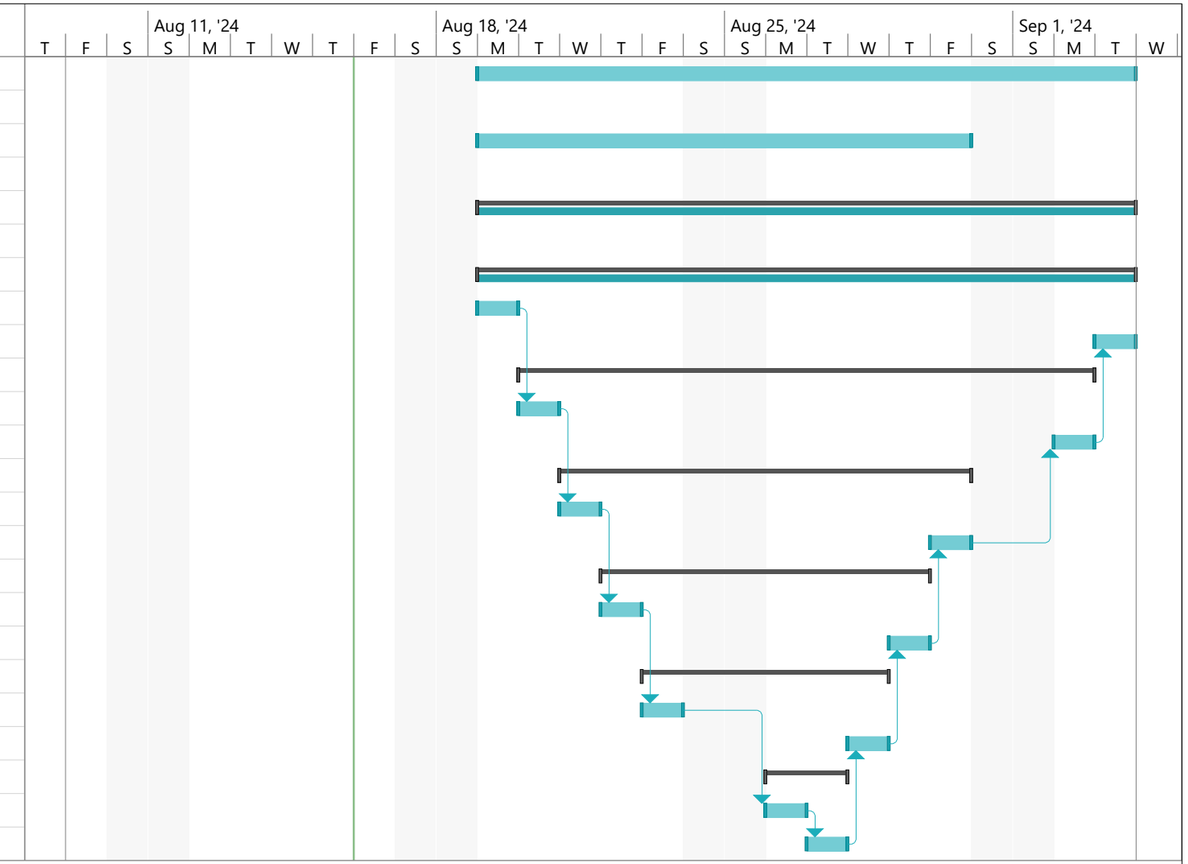

Project: 30261 Two Week Look
Date: Fri 8/16/24

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
